



THE STATE OF NEW HAMPSHIRE
DEPARTMENT OF TRANSPORTATION



20

William Cass, P.E.
Commissioner

David Rodrigue, P.E.
Assistant Commissioner

Her Excellency, Governor Kelly A. Ayotte
and Honorable Council
State House
Concord, New Hampshire 03301

Bureau of Construction
May 8, 2025

REQUESTED ACTION

1. Authorize the Department of Transportation to **retroactively** extend the completion date of Project: Manchester #44501 from May 16, 2025 to June 25, 2025, effective upon Governor and Council approval.
2. Authorize the Department of Transportation to **retroactively** increase the contract value amount for, (Project: Manchester #44501) with C.W. Sliter & Sons, LLC d/b/a CWS Fence & Guardrail Co. (Vendor #155763) of Andover, N.H. by \$216,000 (from \$1,446,755 to \$1,662,755) for guardrail removal and replacement on I-293 through the Millyard in Manchester effective upon Governor and Council approval. 100% Turnpike Funds.

Funding is available as follows:

FY 2025

04-96-96-961017-7025

Turnpike Renewal & Replacement

400-500870 Highway Contract Payments

\$216,000

EXPLANATION

The request is **retroactive** due to added quantities of work discovered within a couple of weeks of original contract completion.

The Manchester 44501 Contract was approved by the Governor and Council on July 10, 2024 (Item # 14) on the basis of a low bid for an original contract encumbrance of \$1,446,755. The contract is proposed to be increased by \$216,000 in accordance with the Standard Specifications to address the following items:

1. The quantity of Limited Reuse Soils (LRS) found in the median is greater than anticipated and requires additional excavation, rehandling, and grading for proper drainage and crash-worthy guardrail installation. The estimated additional cost for this work is \$136,000.
2. The grassed median area impacted by the regrading and guardrail replacement is greater than anticipated and requires additional seeding and turf establishment for erosion control protection and earth stabilization. The estimated additional cost for this work is \$60,000.

3. Additional portable concrete barrier for traffic control with drainage slots is needed for worker safety and drainage relief for driver safety. The estimated additional cost for this work is \$20,000.

Your approval of this resolution is respectfully requested.

Sincerely,

A handwritten signature in cursive script that reads "William Cass".

William J. Cass, P.E.
Commissioner

Attachments

GC



**THE STATE OF NEW HAMPSHIRE
DEPARTMENT OF TRANSPORTATION**



G&C #14
DATE 7/10/24

14

*William Cass, P.E.
Commissioner*

*David Rodrigue, P.E.
Assistant Commissioner
Andre Briere, Colonel, USAF (RET)
Deputy Commissioner*

His Excellency, Governor Christopher T. Sununu
and the Honorable Council
State House
Concord, New Hampshire 03301

Bureau of Construction
April 24, 2024

REQUESTED ACTION

1. Authorize the Department of Transportation to enter into a contract with C.W. Sliter & Sons, LLC d/b/a CWS Fence & Guardrail Co. (Vendor 155763) of Andover, NH, on the basis of a low bid of \$1,446,755 for guardrail removal and replacement on I-293 through the Millyard in Manchester (Project: Manchester #44501), from the date of Governor and Council approval through May 16, 2025, unless amended by the Department in accordance with the Standard Specifications. 100% Turnpike Funds.

Funding is available in State Fiscal Year 2025 as follows:

Funding is available as follows:	<u>FY 2025</u>
04-96-96-961017-7025	
Turnpike Renewal & Replacement	
400-500870 Highway Contract Payments	\$1,446,755

2. Further authorize that a contingency in the amount of \$72,337.75 be approved for payment of latent conditions, which may appear during the construction of the project. The contingency requested is 5% of the contract amount.

Funding is available as follows:	<u>FY 2025</u>
04-96-96-961017-7025	
Turnpike Renewal & Replacement	
400-500870 Highway Contract Payments	\$72,337.75

EXPLANATION

This project is part of the Turnpike's Renewal and Replacement Program. This project is located in the median of I-293 through the Millyard in Manchester, starting 500 ft north of the Bridge Street bridge continuing north to 1,000 ft south of Exit 7 northbound off ramp. Approximately 7,150 feet of box beam guardrail will be removed and replaced with double faced thrie beam guardrail. Concrete barrier pier protection will be constructed at the two bridges located within the project area.

The box beam guardrail located within the median has been in service since approximately 1970. This rail does not perform well, and routine maintenance is difficult. Potential delays in Manchester 16099 project have made replacement of the box beam a higher priority. The project will remove the box beam guardrail

and will replace it with double faced thrie beam. Concrete barrier pier protection will be constructed at the two bridges located within the project area to protect the piers from potential impacts.

The proposed contingency amount is 5% of the contract amount. This project was quantified based on field observations, aerial photos, and as-built plans. Field adjustments may be required due to varying field conditions and unforeseen conditions.

Although the bid costs exceeded the Department's estimate by 39.09%, the low bid of two bids received is felt to be reasonable for the work involved. The items that resulted in the higher than anticipated bid were, Item 606.21203 Double Faced Guardrail \$141,900, Item 646.41 Turf Establishment \$102,000 and Item 203.382 Rehandling LRS \$57,500. Readvertising this project would result, in our opinion, in higher prices and prevent the completion of the work in a timely manner. The Department considers it to be in the best interest of the State to accept this bid to accomplish these needed repairs.

The Contractor has been prequalified by this Department. The Contract has been approved by the Attorney General as to form and execution, and the Department has certified that the necessary funds are available and the bid reasonably conforms to the engineer's estimate in accordance with State procedure. Copies of the fully executed contract are on file at the Secretary of State's Office and the Department of Administrative Service's Office, and subsequent to Governor and Council approval will be on file at the Department of Transportation.

This project funding is: 0% Federal funds (100% Turnpike Renewal and Replacement Program).

A copy of the Tabulation of Bids received for this project is attached along with the Contract Supplemental Sheet and a map indicating the location of the project. .

Sincerely,



William J. Cass, P.E.
Commissioner

WJC/pcj

Department Estimate:	\$1,040,145.00
Contract Amount:	<u>\$1,446,755.00</u>
Over Estimate:	\$ 406,610.00
Attachments	



ABC Bid Data

MANCHESTER
44501
NON-FEDERAL

PROJECT: MANCHESTER
STATE PROJECT NUMBER: 44501
FED. PROJECT NUMBER: NON-FEDERAL
DATE BIDS OPEN: April 18, 2024, 2:00
SCOPE OF WORK: Replacement of box beam along I-293 in Manchester
COMPLETION DATE: October 25, 2024
LOCATION: Hillsborough

Awarded To: C.W. SLITER & SONS LLC
dba CWS FENCE &
GUARDRAIL
261 FRANKLIN HIGHWAY
ANDOVER, NH 03216-3810
Amount: \$1,446,755.00
Award Date:

Certified by: WILLIAM J. OLDENBURG
Director of Project Development

Summary of Bidders

Contractor	Bid Amount	Rank
C.W. SLITER & SONS LLC dba CWS FENCE & GUARDRAIL 261 FRANKLIN HIGHWAY, ANDOVER NH 03216-3810	\$1,446,755.00	A
DELUCCA FENCE COMPANY, INC. 5 OLD FERRY ROAD, METHUEN MA 01844	\$2,116,253.75	B

Item No.	Description	Unit	Quantity	PRICE		C.W. SLITER & SONS LLC dba CWS FENCE & GUARDRAIL 881 FRANKLIN HIGHWAY ANDOVER, NH 03218-3818		DELUCA FENCE COMPANY, INC. 5 OLD FERRY ROAD METHUEN, MA 01844	
				Unit Price	Total	Unit Price	Total	Unit Price	Total

Items

202.7	REMOVAL OF GUARDRAIL	LF	7,150.00	\$3.50	\$25,025.00	\$7.50	\$53,625.00	\$12.50	\$89,375.00
203.11	COMMON EXCAVATION - LRS	CY	500.00	\$30.00	\$15,000.00	\$30.00	\$15,000.00	\$89.25	\$44,625.00
203.382	REHANDLING AND TRANSPORTING LRS	CY	500.00	\$50.00	\$25,000.00	\$165.00	\$82,500.00	\$89.25	\$44,625.00
204.19	COMMON STRUCTURE EXCAVATION EXPLORATORY	CY	50.00	\$250.00	\$12,500.00	\$350.00	\$17,500.00	\$375.00	\$18,750.00
304.1	SAND (F)	CY	87.00	\$55.00	\$3,885.00	\$80.00	\$4,020.00	\$100.00	\$8,700.00
304.32	CRUSHED GRAVEL FOR SHOULDER LEVELING	TON	100.00	\$200.00	\$20,000.00	\$85.00	\$8,500.00	\$100.00	\$10,000.00
520.1	CONCRETE CLASS A	CY	7.00	\$2,250.00	\$15,750.00	\$7,000.00	\$49,000.00	\$2,450.00	\$17,150.00
534.3	WATER REPELLENT (SILANE/SILOXANE)	GAL	35.00	\$125.00	\$4,375.00	\$200.00	\$7,000.00	\$36.75	\$1,286.25
585.7	STONE FILL, CLASS G	CY	11.00	\$150.00	\$1,650.00	\$180.00	\$1,980.00	\$100.00	\$1,100.00
593.121	GEOTEXTILE; SUBSUR DRAIN CL2, NON-WOVEN	SY	3.00	\$20.00	\$60.00	\$10.00	\$30.00	\$315.00	\$945.00
603.60204	6" PLASTIC PIPE (SMOOTH INTERIOR)	LF	220.00	\$75.00	\$16,500.00	\$75.00	\$16,500.00	\$145.00	\$31,900.00
606.21203	DOUBLE-FACED BEAM GUARDRAIL (THRE BEAM) (STEEL POST)	LF	4,450.00	\$75.00	\$483,750.00	\$97.00	\$625,650.00	\$88.75	\$657,237.50
606.322	DOUBLE FACED TRANSITION RAIL, STEEL POST	U	8.00	\$7,500.00	\$60,000.00	\$8,175.00	\$49,400.00	\$8,825.00	\$70,600.00
606.41252	64" SINGLE SLOPE CONCRETE BARRIER (PRECAST) TRANSITION TO BEAM GUARDRAIL	U	6.00	\$7,500.00	\$45,000.00	\$8,750.00	\$52,500.00	\$29,925.00	\$178,550.00
606.4135	64" SINGLE SLOPE CONCRETE BARRIER, PRECAST	LF	220.00	\$225.00	\$49,500.00	\$225.00	\$49,500.00	\$2,047.50	\$450,450.00
606.417	PORTABLE CONCRETE BARRIER FOR TRAFFIC CONTROL	LF	100.00	\$250.00	\$25,000.00	\$300.00	\$30,000.00	\$504.00	\$50,400.00
618.61	UNIFORMED OFFICERS WITH VEHICLE	\$	30,000.00	\$1.00	\$30,000.00	\$1.00	\$30,000.00	\$1.00	\$30,000.00
618.1	MAINTENANCE OF TRAFFIC	U	1.00	\$35,000.00	\$35,000.00	\$65,000.00	\$65,000.00	\$100,000.00	\$100,000.00
618.25	PORTABLE CHANGEABLE MESSAGE SIGN	U	4.00	\$5,000.00	\$20,000.00	\$1,500.00	\$6,000.00	\$10,265.00	\$41,080.00
618.379	AUTOMATED TRAILER-MOUNTED SPEED LIMIT SIGN	U	2.00	\$5,000.00	\$10,000.00	\$3,000.00	\$6,000.00	\$10,265.00	\$20,530.00
618.63	TRUCK-MOUNTED IMPACT ATTENUATOR, TEST LEVEL 3	U	2.00	\$7,500.00	\$15,000.00	\$2,500.00	\$5,000.00	\$9,000.00	\$18,000.00
621.1	RETROREFLECTIVE MEDIAN BARRIER DELINEATOR	EA	20.00	\$55.00	\$1,100.00	\$50.00	\$1,000.00	\$54.00	\$1,080.00
621.3312	SINGLE LARGE DELINEATOR DOUBLE FACED WITH POST	EA	30.00	\$100.00	\$3,000.00	\$85.00	\$2,550.00	\$73.00	\$2,190.00
644.41	TURF ESTABLISHMENT WITH MULCH, TACKIFIERS AND HUMUS	SY	6,800.00	\$5.00	\$42,500.00	\$17.00	\$144,500.00	\$20.00	\$170,000.00

ABC Bid Data

MANCHESTER
 44501
 NON-FEDERAL

Item No.	Description	Unit	Quantity	P&A		C.W. BUTER & SONS LLC dba CWS FENCE & GUARDRAIL 391 FRANKLIN HIGHWAY ANDOVER, NH 03110-3610		DELIJOCA FENCE COMPANY, INC. 5 OLD PERRY ROAD BETHLEHEM, MA 01804	
				Unit Price	Total	Unit Price	Total	Unit Price	Total
692.	MOBILIZATION	U	1.00	\$45,000.00	\$45,000.00	\$87,500.00	\$87,500.00	\$100,000.00	\$100,000.00
697.31	PROJECT OPERATIONS PLAN	U	1.00	\$5,750.00	\$5,750.00	\$8,500.00	\$8,500.00	\$13,500.00	\$13,500.00
699.	MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL	\$	10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00
1008.11	ALTERATIONS AND ADDITIONS AS NEEDED - UNANTICIPATED WORK	\$	10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00
1016.15	FUEL ADJUSTMENT	\$	10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00
Totals:					\$1,040,143.00		\$1,448,765.00		\$2,116,253.75
Alt. Totals:									
Totals:					\$1,040,143.00		\$1,448,765.00		\$2,116,253.75



PS&E Comparison

MANCHESTER
44501
NON-FEDERAL

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
Items								
202.7	REMOVAL OF GUARDRAIL	LF	7,150.00	\$7.50	\$53,625.00	\$3.50	\$25,025.00	\$28,600.00
203.11	COMMON EXCAVATION - LRS	CY	500.00	\$30.00	\$15,000.00	\$30.00	\$15,000.00	\$0.00
203.382	REHANDLING AND TRANSPORTING LRS	CY	500.00	\$165.00	\$82,500.00	\$50.00	\$25,000.00	\$57,500.00
206.19	COMMON STRUCTURE EXCAVATION EXPLORATORY	CY	50.00	\$350.00	\$17,500.00	\$250.00	\$12,500.00	\$5,000.00
304.1	SAND (F)	CY	67.00	\$60.00	\$4,020.00	\$55.00	\$3,685.00	\$335.00
304.32	CRUSHED GRAVEL FOR SHOULDER LEVELING	TON	100.00	\$65.00	\$6,500.00	\$200.00	\$20,000.00	(\$13,500.00)
520.1	CONCRETE CLASS A	CY	7.00	\$7,000.00	\$49,000.00	\$2,250.00	\$15,750.00	\$33,250.00
534.3	WATER REPELLENT (SILANE/SILOXANE)	GAL	35.00	\$200.00	\$7,000.00	\$125.00	\$4,375.00	\$2,625.00
585.7	STONE FILL, CLASS G	CY	11.00	\$180.00	\$1,980.00	\$150.00	\$1,650.00	\$330.00
593.121	GEOTEXTILE; SUBSUR DRAIN CL.2, NON-WOVEN	SY	3.00	\$10.00	\$30.00	\$20.00	\$60.00	(\$30.00)
603.80206	6" PLASTIC PIPE (SMOOTH INTERIOR)	LF	220.00	\$75.00	\$16,500.00	\$75.00	\$16,500.00	\$0.00
606.21203	DOUBLE-FACED BEAM GUARDRAIL (THRIE BEAM) (STEEL POST)	LF	6,450.00	\$97.00	\$625,650.00	\$75.00	\$483,750.00	\$141,900.00
606.322	DOUBLE FACED TRANSITION RAIL, STEEL POST	U	8.00	\$6,175.00	\$49,400.00	\$7,500.00	\$60,000.00	(\$10,600.00)
606.41252	54" SINGLE SLOPE CONCRETE BARRIER (PRECAST) TRANSITION TO BEAM GUARDRAIL	U	6.00	\$8,750.00	\$52,500.00	\$7,500.00	\$45,000.00	\$7,500.00

PS&E Comparison

MANCHESTER
 44501
 NON-FEDERAL

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
606.4135	54" SINGLE SLOPE CONCRETE BARRIER, PRECAST	LF	220.00	\$225.00	\$49,500.00	\$225.00	\$49,500.00	\$0.00
606.417	PORTABLE CONCRETE BARRIER FOR TRAFFIC CONTROL	LF	100.00	\$300.00	\$30,000.00	\$250.00	\$25,000.00	\$5,000.00
618.61	UNIFORMED OFFICERS WITH VEHICLE	\$	30,000.00	\$1.00	\$30,000.00	\$1.00	\$30,000.00	\$0.00
619.1	MAINTENANCE OF TRAFFIC	U	1.00	\$65,000.00	\$65,000.00	\$35,000.00	\$35,000.00	\$30,000.00
619.25	PORTABLE CHANGEABLE MESSAGE SIGN	U	4.00	\$1,500.00	\$6,000.00	\$5,000.00	\$20,000.00	(\$14,000.00)
619.279	AUTOMATED TRAILER-MOUNTED SPEED LIMIT SIGN	U	2.00	\$3,000.00	\$6,000.00	\$5,000.00	\$10,000.00	(\$4,000.00)
619.63	TRUCK-MOUNTED IMPACT ATTENUATOR, TEST LEVEL 3	U	2.00	\$2,500.00	\$5,000.00	\$7,500.00	\$15,000.00	(\$10,000.00)
621.1	RETROREFLECTIVE MEDIAN BARRIER DELINEATOR	EA	20.00	\$50.00	\$1,000.00	\$55.00	\$1,100.00	(\$100.00)
621.3312	SINGLE LARGE DELINEATOR DOUBLE FACED WITH POST	EA	30.00	\$85.00	\$2,550.00	\$100.00	\$3,000.00	(\$450.00)
646.41	TURF ESTABLISHMENT WITH MULCH, TACKIFIERS AND HUMUS	SY	8,500.00	\$17.00	\$144,500.00	\$5.00	\$42,500.00	\$102,000.00
692.	MOBILIZATION	U	1.00	\$87,500.00	\$87,500.00	\$45,000.00	\$45,000.00	\$42,500.00
697.31	PROJECT OPERATIONS PLAN	U	1.00	\$8,500.00	\$8,500.00	\$5,750.00	\$5,750.00	\$2,750.00
699.	MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL	\$	10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00	\$0.00
1008.11	ALTERATIONS AND ADDITIONS AS NEEDED - UNANTICIPATED WORK	\$	10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00	\$0.00
1010.15	FUEL ADJUSTMENT	\$	10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00	\$0.00
Total:					\$1,446,755.00		\$1,040,145.00	\$406,610.00

March 26, 2024

SUPPLEMENTAL PROJECT INFORMATION SHEET

DESCRIPTION: This project is located in the median of I-293 through the Millyard in Manchester, starting 500 ft north of the Bridge Street bridge continuing north to 1,000 ft south of Exit 7 northbound off ramp. Approximately 7150 feet of box beam guardrail will be removed and replaced with double faced thrie beam guardrail. Concrete barrier pier protection will be constructed at the two bridges located within the project area.

FEDERAL FUNDING: 0% (100% Turnpike Renewal and Replacement Program)

CONTINGENCY: The proposed contingency amount is 5% of the contract amount. This project was quantified based on field observations, aerial photos, and as-built plans. Field adjustments may be required due to varying field conditions and unforeseen conditions.


PROJECT INITIATED: Bureau of Turnpikes Renewal and Replacement (TRR) Program

PROJECT EXPLANATION: The box beam guardrail located within the median has been in service since approximately 1970. This rail does not perform well, and routine maintenance is difficult. Potential delays in Manchester 16099 project have made replacement of the box beam a higher priority. The project will remove the box beam guardrail and will replace it with double faced thrie beam. Concrete barrier pier protection will be constructed at the two bridges located within the project area to protect the piers from potential impacts.

TRAFFIC IMPLICATIONS: All median work on I-293 will allow a single lane closure northbound and a single lane closure southbound Sunday through Thursday, 9 PM – 5 AM. This will ensure a safer working environment for construction and the traveling public.

COMPLETION DATE: October 25, 2024

MANCHESTER - FE EVERETT TURNPIKE

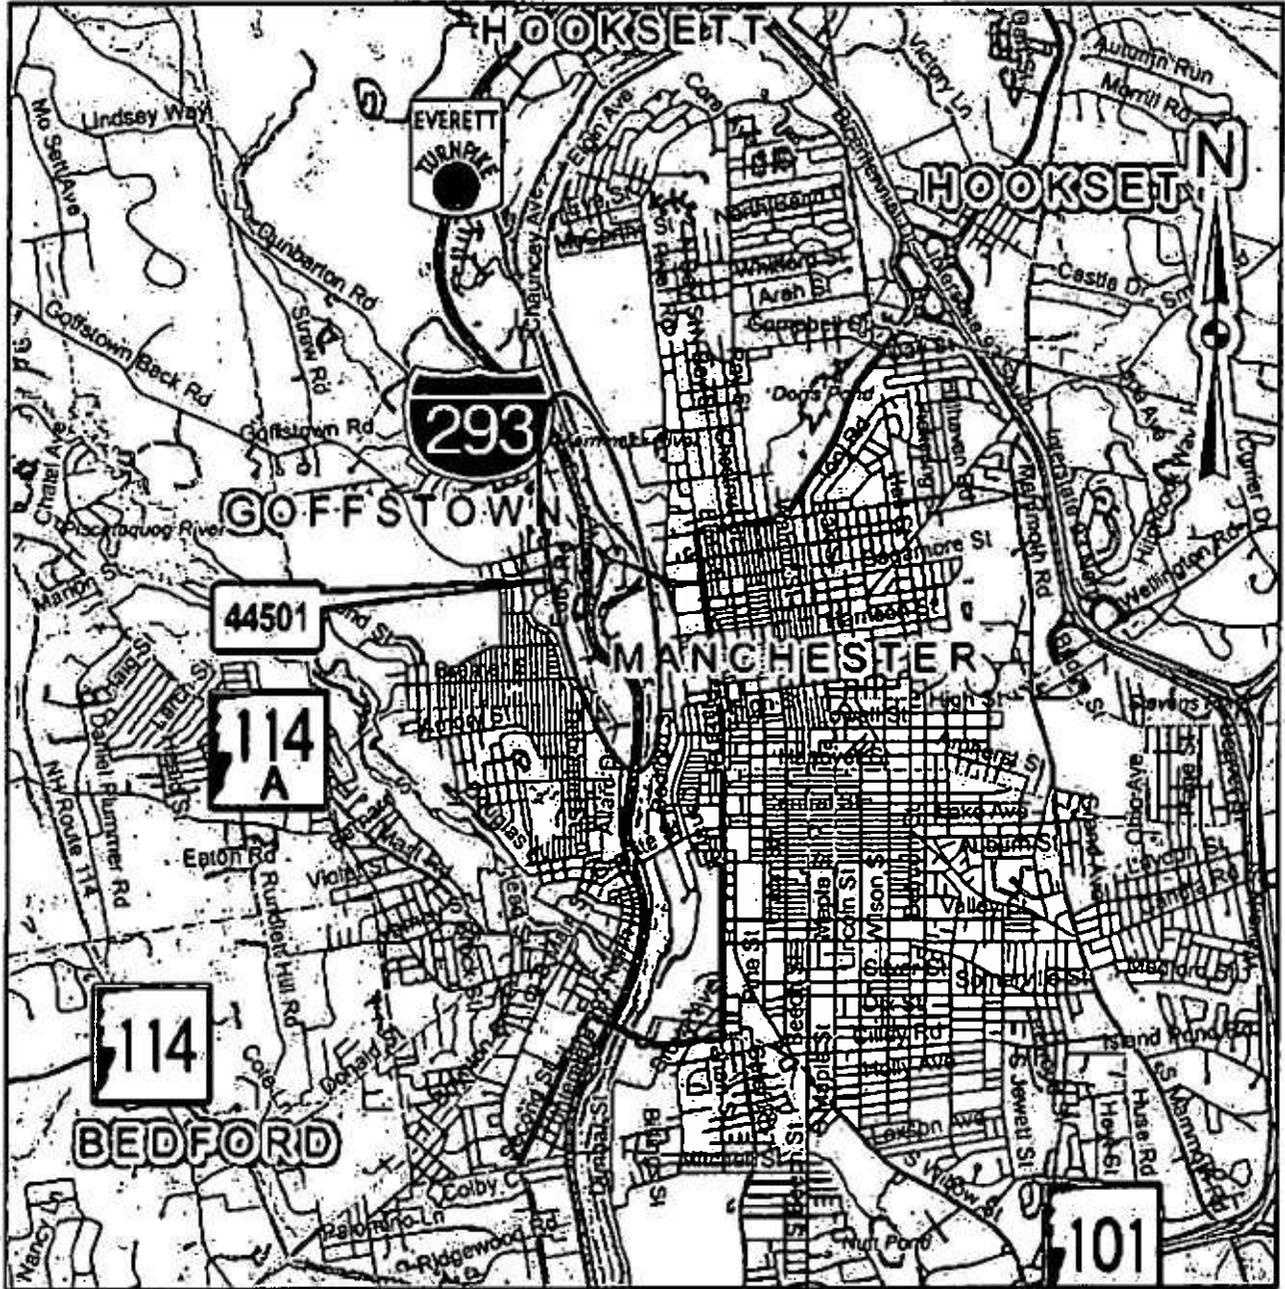


LEGEND

- Streams
- Water Bodies
- US Routes
- State Routes
- Interstates
- Local Roads
- Town Boundary

New Hampshire
DOT
 Department of Transportation

State #: 44501
 Federal #: N/A

LOCATION MAP

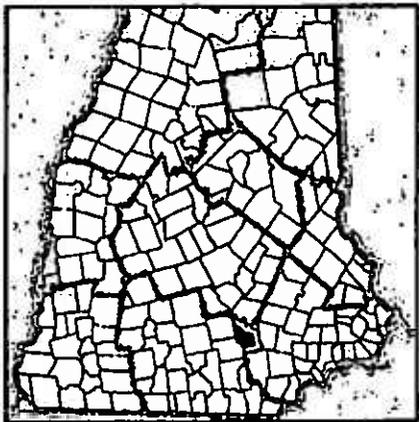

State of New Hampshire

Department of State

CERTIFICATE

I, David M. Scanlan, Secretary of State of the State of New Hampshire, do hereby certify that C.W. SLITER & SONS, LLC is a New Hampshire Limited Liability Company registered to transact business in New Hampshire on January 17, 1984. I further certify that all fees and documents required by the Secretary of State's office have been received and is in good standing as far as this office is concerned.

Business ID: 74644

Certificate Number: 0006660407



IN TESTIMONY WHEREOF,
I hereto set my hand and cause to be affixed
the Seal of the State of New Hampshire,
this 5th day of April A.D. 2024.

A handwritten signature in black ink, appearing to read "D. Scanlan", is written over a circular stamp.

David M. Scanlan
Secretary of State

CERTIFICATE OF VOTE

I, Robert M. Carroll, Jr. Hereby certify that I am duly elected
Member of C.W. Sliter & Sons, LLC dba
CWS Fence & Guardrail Co.

I hereby certify the following is a true copy of a vote taken at a meeting
of the Board of Directors of the Corporation, duly called and held
on April 26, 2024, at which a quorum of the Board was present
and voting.

VOTED: That Robert M. Carroll is duly authorized
to enter into a specific contract namely MANCHESTER 44501
With State of New Hampshire, and further authorized to
Department of Transportation
execute any documents which may in his judgment be desirable or necessary to effect
the purpose of this vote.

I hereby certify that said vote has not been amended or repealed and remains
in full force and effect as of April 26, 2024, and that
Robert M. Carroll is duly elected Managing of this
Member

Corporation.

DATED: April 26, 2024

ATTEST:  (Affix Corp. Seal)
Robert M. Carroll, Jr., Member



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)
4/26/2024

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER THE ROWLEY AGENCY LLC 45 Constitution Avenue P.O. Box 511 Concord NH 03302-0511		CONTACT NAME: Donna Bickford PHONE (AC, No. Ext): (603) 224-2562 E-MAIL ADDRESS: dbickford@rowleyagency.com FAX (AC, No): (603) 224-0012	
INSURED C.W. Bliter & Sons, LLC dba CWS Fence & Guardrail Co. PO Box 120 Andover NH 03216		INSURER(S) AFFORDING COVERAGE	
		INSURER A: Union Insurance Company	NAIC # 25844
		INSURER B: Acadia Insurance Company	NAIC # 31325
		INSURER C:	
		INSURER D:	
		INSURER E:	
		INSURER F:	

COVERAGES **CERTIFICATE NUMBER:** 2024-25 All Lines **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSUR LTR	TYPE OF INSURANCE	ADOL (SUBR) (NSD) (WVD)	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PROJECT <input type="checkbox"/> LOC OTHER:		CPA5540337	1/1/2024	1/1/2025	EACH OCCURRENCE \$ 1,000,000 DAMAGE TO RENTED PREMISES (EA OCCURRENCE) \$ 300,000 MED EXP (Any one person) \$ 10,000 PERSONAL & ADV INJURY \$ 1,000,000 GENERAL AGGREGATE \$ 2,000,000 PRODUCTS - COMPROP AGG \$ 2,000,000
A	AUTOMOBILE LIABILITY <input checked="" type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> HIRED AUTOS <input type="checkbox"/> NON-OWNED AUTOS		CAA5540338	1/1/2024	1/1/2025	COMBINED SINGLE LIMIT (EA ACCIDENT) \$ 1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$
B	<input checked="" type="checkbox"/> UMBRELLA LIAB <input checked="" type="checkbox"/> OCCUR <input type="checkbox"/> EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE DED <input checked="" type="checkbox"/> RETENTION \$ 0		CUA5540339	1/1/2024	1/1/2025	EACH OCCURRENCE \$ 5,000,000 AGGREGATE \$ 5,000,000 PRODUCTS/COMPROP AGG \$ 5,000,000
B	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below	Y/N N N/A	WCA5540340	1/1/2024	1/1/2025	<input checked="" type="checkbox"/> PER STATUTE <input type="checkbox"/> OTHER E.L. EACH ACCIDENT \$ 500,000 E.L. DISEASE - EA EMPLOYEE \$ 500,000 E.L. DISEASE - POLICY LIMIT \$ 500,000
A	LEASED/RENTED EQUIPMENT		CPA5540337	1/1/2024	1/1/2025	LIMIT \$ 50,000 DEDUCTIBLE \$ 250

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 107, Additional Remarks Schedule, may be attached if more space is required)
REF: 44501- Replacement of box beam along I-293 in Manchester. Following applies when required by written contract with the named insured: State of NH- Dept. of Transportation is included as add'l insured on all liability policies except workers comp on a primary/noncontributory basis. Waiver of Subrogation in favor of AI applies except workers comp.

CERTIFICATE HOLDER State of NH- Dept. of Transportation PO Box 483 Concord, NH 03302	CANCELLATION SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS. AUTHORIZED REPRESENTATIVE Donna Bickford/DTB <i>Donna Bickford</i>
--	--



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)

5/8/2024

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).


PRODUCER THE ROWLEY AGENCY 45 Constitution Avenue P.O. Box 511 Concord NH 03302-0511	CONTACT NAME: Donna Bickford PHONE (AG, No. Ext.): (603) 224-2562 FAX (AG, No.): (603) 224-0013 E-MAIL ADDRESS: dbickford@rowleyagency.com
	INSURER(S) AFFORDING COVERAGE NAIC # INSURER A: Acadia Insurance Company 31325 INSURER B: INSURER C: INSURER D: INSURER E: INSURER F:

COVERAGES CERTIFICATE NUMBER: OCP NHDOT #44501 REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADOL. INSD	AUTR. INSD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR <input checked="" type="checkbox"/> Owners & Contractors Protec GEN'L AGGREGATE LIMIT APPLIES PER: <input checked="" type="checkbox"/> POLICY <input type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC OTHER:			OCFB2442615794	5/29/2024	5/29/2025	EACH OCCURRENCE \$ 2,000,000 DAMAGE TO RENTED PREMISES (Per occurrence) \$ MED EXP (Any one person) \$ PERSONAL & ADV INJURY \$ GENERAL AGGREGATE \$ 3,000,000 PRODUCTS - COMPOP AGG \$ OTHER \$
	AUTOMOBILE LIABILITY <input type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> HIRED AUTOS <input type="checkbox"/> NON-OWNED AUTOS						COMBINED SINGLE LIMIT (Per accident) \$ BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ OTHER \$
	UMBRELLA LIAB <input type="checkbox"/> OCCUR EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE DED <input type="checkbox"/> RETENTION \$						EACH OCCURRENCE \$ AGGREGATE \$ OTHER \$
	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below						<input type="checkbox"/> PER STATUTE <input type="checkbox"/> OTHER E.L. EACH ACCIDENT \$ E.L. DISEASE - EA EMPLOYEE \$ E.L. DISEASE - POLICY LIMIT \$

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)
 Re: Manchester #44501/ Median of I-293 Guardrail Replacement through The Millyard

CERTIFICATE HOLDER New Hampshire-Dept. of Transportation PO Box 483 Concord, NH 03302-0483	CANCELLATION SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS. AUTHORIZED REPRESENTATIVE Donna Bickford/DTB 
--	--

© 1988-2014 ACORD CORPORATION. All rights reserved.
