



SEP 02 10 58 AM '15  
**THE STATE OF NEW HAMPSHIRE**  
**DEPARTMENT OF TRANSPORTATION**



Blank  
26

**WILLIAM CASS, P.E.**  
**ASSISTANT COMMISSIONER**

Bureau of Construction  
August 11, 2015

Her Excellency, Governor Margaret Wood Hassan  
and the Honorable Council  
State House  
Concord, New Hampshire 03301

**REQUESTED ACTION**

1. Authorize the Department of Transportation to enter into a contract with D.R. Key Corporation (Vendor 155720) of Lebanon, NH on the basis of a low bid of \$169,865.50 for pedestrian safety improvements at the intersection of NH Route 10, Oak Ridge Road and Gould Road in Lebanon, from the date of Governor and Council approval through June 10, 2016 unless extended by the Department in accordance with the Standard Specifications. 100% Federal Funds.

Funds to support this request are anticipated to be available in the following accounts in State FY 2016 upon the availability and continued appropriation of funds in the future operating budget, with the ability to adjust encumbrances between State Fiscal Years through the Budget Office, if needed and justified:

Funding is available as follows: FY 2016  
04-96-96-963515-3054  
Consolidated Federal Aid  
400-500870 Highway Contract Payments \$169,865.50

2. Further authorize that a contingency in the amount of \$11,890.59 be approved for payment of latent conditions, which may appear during the construction of the project. The contingency requested is 7% of the contract amount.

Funding is available as follows: FY 2016  
04-96-96-963515-3054  
Consolidated Federal Aid  
400-500870 Highway Contract Payments \$11,890.59

**EXPLANATION**

This project is part of the annual Highway Safety Improvement Program. A pedestrian fatality occurred at the intersection in 2013 and after a Road Safety Audit was completed in February 2014, proposed improvements as outlined in the project scope were recommended at the subject intersection. Improvements include constructing a raised median island with American Disability Act (ADA) accessibility, crosswalk, curbing and sidewalk ramps, enhanced lighting, and pedestrian activated rectangular rapid flashing beacons. Also included is a 1" overlay and new pavement markings for the project area.

The contingency amount is proposed to be 7% of the contract amount is necessary to address any latent field conditions. This is a short duration project with a relatively small contract value, and potential fuel and asphalt adjustments need to be considered.

Although the bid costs exceeded the Department's estimate, the low bid is felt to be reasonable for the work involved and likely the result of a fairly aggressive schedule to complete a significant portion of work prior to the intermediate completion date this fall. Re-advertising this project would result, in our opinion, in higher prices and prevent the completion of the work in a timely manner. The Department considers it to be in the best interest of the State to accept this bid to accomplish these needed repairs.

The Contractor has been prequalified by this Department. The Contract has been approved by the Attorney General as to form and execution, and the Department has certified that the necessary funds are available and that the bid reasonably conforms to the engineer's estimate in accordance with State procedure. Copies of the fully executed contract are on file at the Secretary of State's Office and the Department of Administrative Service's Office, and subsequent to Governor and Council approval will be on file at the Department of Transportation.

This project funding is 90% federal funds with 10% state match. Turnpike toll credits are being utilized for match requirements, effectively using 100% federal funds.

A copy of the Tabulation of Bids received for this project is attached along with the Contract Supplemental Sheet and a map indicating the location of the project.

Sincerely,



William J. Cass, P.E.  
Assistant Commissioner

WJC/md

|                      |                     |
|----------------------|---------------------|
| Department Estimate: | \$140,415.00        |
| Contract Amount:     | <u>\$169,865.50</u> |
| Over Estimate:       | \$ 29,450.50        |

Attachments

June 15, 2015

## SUPPLEMENTAL PROJECT INFORMATION SHEET

**DESCRIPTION:** This project involves pedestrian safety improvements at the intersection of NH Route 10, Oak Ridge Road and Gould Road. The limits of construction on NH Route 10 are approximately 400' South to 600' North of the crosswalk. Improvements to this pedestrian crossing include pedestrian activated rectangular rapid flashing beacons, a raised median island with a crosswalk cut through, enhanced lighting, and curbing and sidewalk ramps. The work also includes a 1" overlay and new pavement markings for the project area.

**FEDERAL FUNDING:** 90% (HSIP) with anticipated utilization of Turnpike Toll Credits for the State's 10% match.

**CONTINGENCY:** The proposed contingency amount is 7% of the contract amount. This is short duration project with a relatively small contract value. Adjusting limits to offset quantity overruns is not practical, and potential fuel and asphalt adjustments need to be considered.




**PROJECT INITIATED:** State's 10-Year Transportation Improvement Plan

**PROJECT EXPLANATION:** A pedestrian fatality occurred at the intersection in 2013 and after a Road Safety Audit was completed in February 2014, Concept 1 was chosen as the project scope. Improvements to the intersection include constructing a raised median island with a crosswalk cut through, curbing and sidewalk ramps, enhanced lighting, and pedestrian activated rectangular rapid flashing beacons. Also included is a 1" overlay and new pavement markings for the project area.

**TRAFFIC IMPLICATION:** This will be a short duration construction project, approximately 30 working days, with 3 phases that will require periods of one lane, alternating two way traffic to construct the median island and for final paving and striping. Traffic will be returned to two way operation during non-work hours.


**INTERMEDIATE COMPLETION DATE:** November 13, 2015 for all work except final paving and pavement markings.

**FINAL COMPLETION DATE:** June 10, 2016.

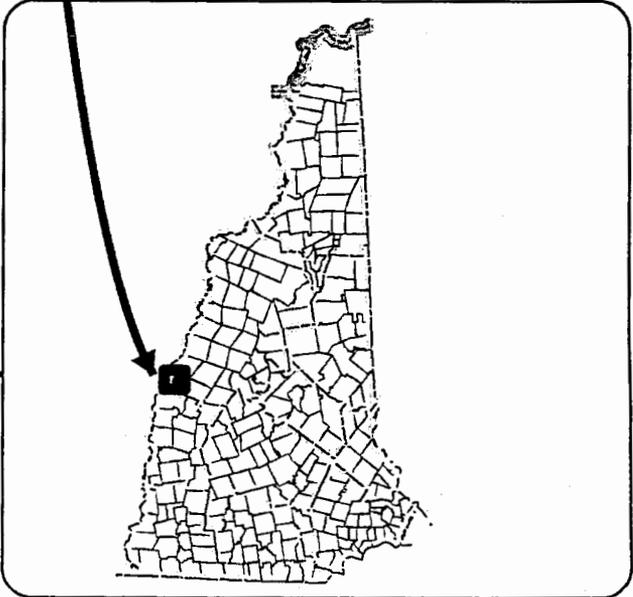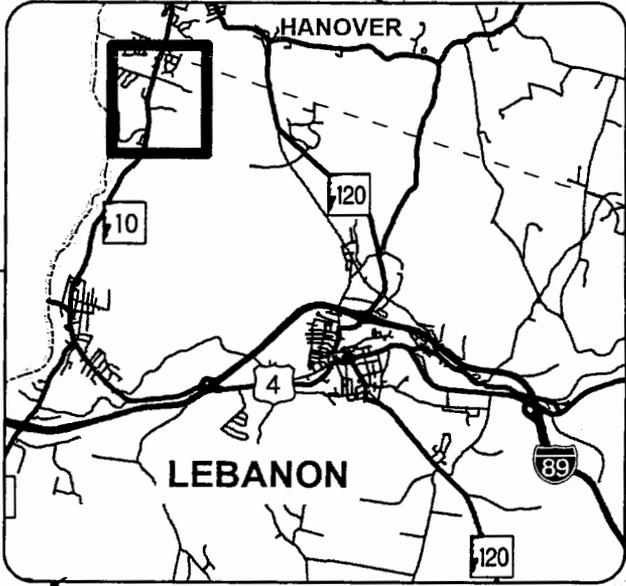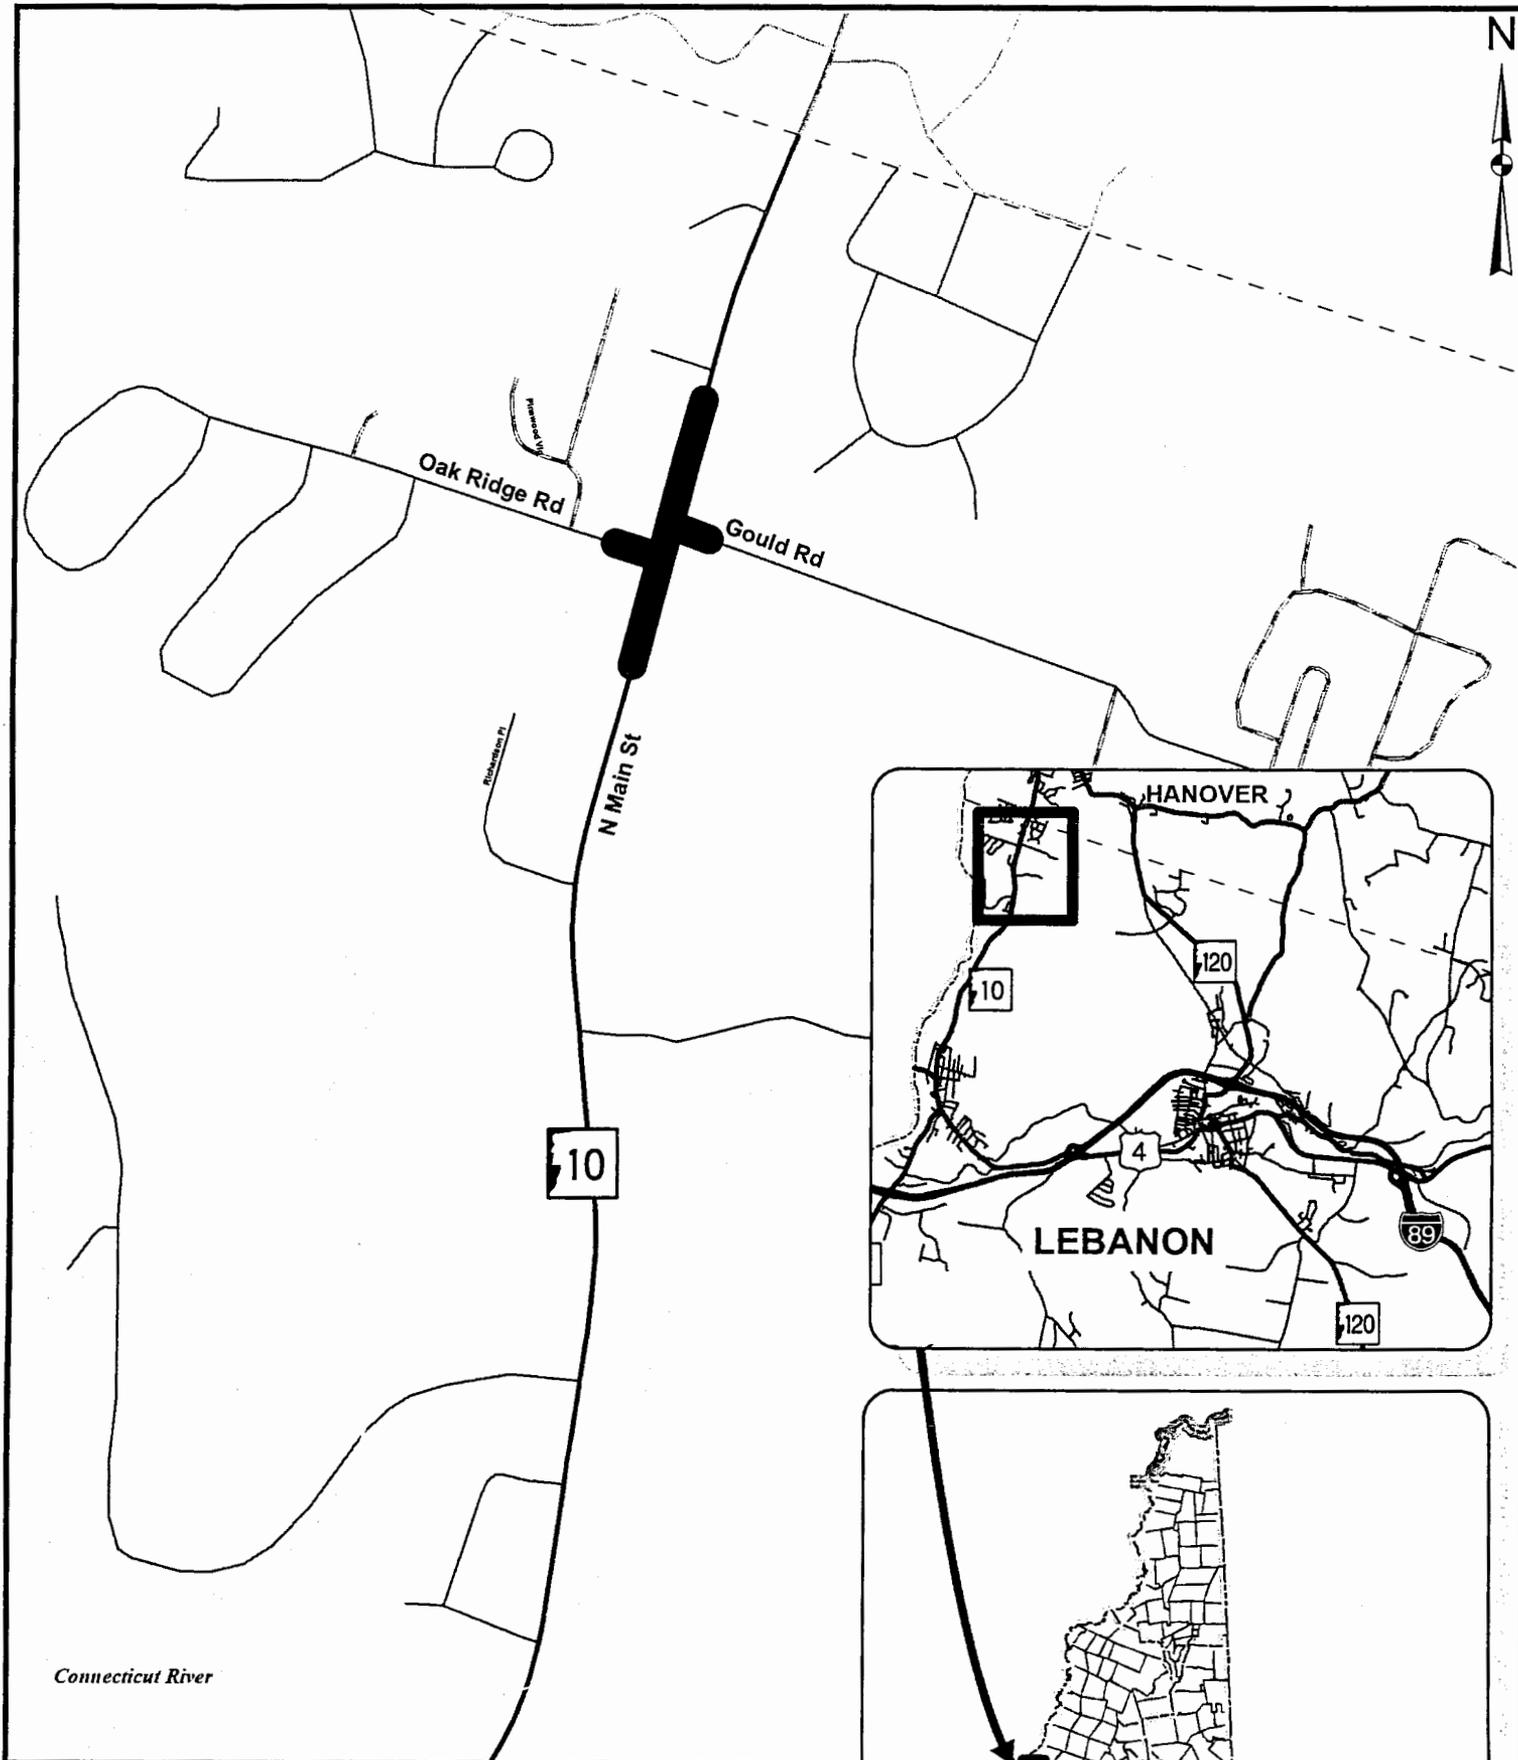

# LEBANON 29362

X-A004(065) -PEDESTRIAN SAFETY IMPROVEMENT  
NH 10 / OAK RIDGE ROAD / GOULD RD



**State of New Hampshire  
Department of Transportation**

**Project:** LEBANON X-A004(065) 29362  
**County and Code:** GRAFTON COUNTY 009  
**Date Bids Open:** July 23, 2015  
**Scope of Work:** PEDESTRIAN SAFETY IMPROVEMENTS  
**Location:** NH ROUTE 10, OAK RIDGE ROAD AND GOULD ROAD  
**Completion Date:** June 10, 2016

A D R KEY CORPORATION  
255 DARTMOUTH COLLEGE HWY LEBANON NH 03766

B L & M SERVICE CONTRACTORS, LLC  
126 ROUTE 10 ORFORD, NH 03777

\$169,865.50

\$199,159.00

| Item No. | Description                             | Unit | Quantity | A          |             | B           |             |
|----------|---|------|----------|------------|-------------|-------------|-------------|
|          |   |      |          | Unit Price | Total       | Unit Price  | Total       |
| 203.1    | COMMON EXCAVATION                       | CY   | 25.00    | \$60.00    | \$1,500.00  | \$65.00     | \$1,625.00  |
| 203.2    | ROCK EXCAVATION                         | CY   | 9.00     | \$150.00   | \$1,350.00  | \$100.00    | \$900.00    |
| 203.6    | EMBANKMENT-IN-PLACE (F)                 | CY   | 10.00    | \$45.00    | \$450.00    | \$65.00     | \$650.00    |
| 206.19   | COMMON STRUCTURE EXCAVATION EXPLORATORY | CY   | 5.00     | \$75.00    | \$375.00    | \$65.00     | \$325.00    |
| 214      | FINE GRADING                            | U    | 1.00     | \$1,800.00 | \$1,800.00  | \$10,000.00 | \$10,000.00 |
| 304.301  | CRUSHED GRAVEL                          | CY   | 25.00    | \$95.00    | \$2,375.00  | \$65.00     | \$1,625.00  |
| 304.32   | CRUSHED GRAVEL FOR SHOULDER LEVELING    | TON  | 25.00    | \$95.00    | \$2,375.00  | \$50.00     | \$1,250.00  |
| 403.11   | HOT BITUMINOUS PAVEMENT, MACHINE METHOD | TON  | 240.00   | \$160.00   | \$38,400.00 | \$160.00    | \$38,400.00 |
| 403.12   | HOT BITUMINOUS PAVEMENT, HAND METHOD    | TON  | 10.00    | \$165.00   | \$1,650.00  | \$160.00    | \$1,600.00  |
| 403.6    | PAVEMENT JOINT ADHESIVE                 | LF   | 2,220.00 | \$2.30     | \$5,106.00  | \$2.25      | \$4,995.00  |
| 417      | COLD PLANING BITUMINOUS SURFACES        | SY   | 210.00   | \$32.00    | \$6,720.00  | \$35.00     | \$7,350.00  |
| 604.51   | RECONSTRUCTING/ADJUSTING SEWER MANHOLES | LF   | 1.00     | \$750.00   | \$750.00    | \$1,500.00  | \$1,500.00  |
| 608.12   | 2" BITUMINOUS SIDEWALK (F)              | SY   | 25.00    | \$53.00    | \$1,325.00  | \$50.00     | \$1,250.00  |
| 608.24   | 4" CONCRETE SIDEWALK (F)                | SY   | 35.00    | \$65.00    | \$2,275.00  | \$85.00     | \$2,975.00  |
| 608.26   | 6" CONCRETE SIDEWALK (F)                | SY   | 30.00    | \$70.00    | \$2,100.00  | \$85.00     | \$2,550.00  |
| 608.54   | DETECTABLE WARNING DEVICES, CAST IRON   | SY   | 8.00     | \$450.00   | \$3,600.00  | \$250.00    | \$2,000.00  |
| 609.01   | STRAIGHT GRANITE CURB                   | LF   | 15.00    | \$42.00    | \$630.00    | \$36.00     | \$540.00    |
| 609.216  | STRAIGHT GRANITE SLOPE CURB 6" HIGH     | LF   | 95.00    | \$40.00    | \$3,800.00  | \$36.00     | \$3,420.00  |
| 609.236  | CURVED GRANITE SLOPE CURB 6" HIGH       | LF   | 25.00    | \$105.00   | \$2,625.00  | \$36.00     | \$900.00    |
| 609.5    | RESET GRANITE CURB                      | LF   | 39.00    | \$24.00    | \$936.00    | \$32.00     | \$1,248.00  |

| Item No. | Description  | Unit | Quantity | A           |             | B           |             |
|----------|--|------|----------|-------------|-------------|-------------|-------------|
|          |  |      |          | Unit Price  | Total       | Unit Price  | Total       |
| 615.03   | TRAFFIC SIGN TYPE C (F)                                    | SF   | 42.00    | \$66.00     | \$2,772.00  | \$60.00     | \$2,520.00  |
| 615.06   | TRAFFIC SIGN TYPE CC (F)                                   | SF   | 14.00    | \$22.00     | \$308.00    | \$30.00     | \$420.00    |
| 616.261  | RECTANGULAR RAPID FLASHING BEACON                          | U    | 1.00     | \$21,000.00 | \$21,000.00 | \$20,000.00 | \$20,000.00 |
| 618.7    | FLAGGERS   | HR   | 240.00   | \$35.00     | \$8,400.00  | \$22.00     | \$5,280.00  |
| 619.1    | MAINTENANCE OF TRAFFIC                                     | U    | 1.00     | \$15,000.00 | \$15,000.00 | \$10,000.00 | \$10,000.00 |
| 619.25   | PORTABLE CHANGEABLE MESSAGE SIGN                           | U    | 2.00     | \$4,000.00  | \$8,000.00  | \$2,000.00  | \$4,000.00  |
| 621.31   | SINGLE DELINEATOR WITH POST                                | EA   | 3.00     | \$85.00     | \$255.00    | \$100.00    | \$300.00    |
| 628.1    | SAWED CONCRETE PAVEMENT                                    | LF   | 122.00   | \$6.00      | \$732.00    | \$3.00      | \$366.00    |
| 628.2    | SAWED BITUMINOUS PAVEMENT                                  | LF   | 80.00    | \$3.00      | \$240.00    | \$3.00      | \$240.00    |
| 632.0104 | RETROREFLECTIVE PAINT PAVE. MARKING, 4" LINE               | LF   | 9,400.00 | \$0.30      | \$2,820.00  | \$0.25      | \$2,350.00  |
| 632.0112 | RETROREFLECTIVE PAINT PAVE. MARKING, 12" LINE              | LF   | 125.00   | \$1.40      | \$175.00    | \$3.50      | \$437.50    |
| 632.3104 | RETROREFLECT. THERMOPLAS. PAVE. MARKING, 4" LINE           | LF   | 105.00   | \$3.30      | \$346.50    | \$3.50      | \$367.50    |
| 632.3112 | RETROREFLECT. THERMOPLAS. PAVE. MARKING, 12" LINE          | LF   | 70.00    | \$5.50      | \$385.00    | \$3.50      | \$245.00    |
| 632.3118 | RETROREFLECT. THERMOPLAS. PAVE. MARKING, 18" LINE          | LF   | 50.00    | \$7.70      | \$385.00    | \$4.50      | \$225.00    |
| 632.32   | RETROREFLECT. THERMOPLAS. PAVEMENT MARKING, SYMBOL OR WORD | SF   | 40.00    | \$11.00     | \$440.00    | \$13.00     | \$520.00    |
| 632.911  | OBLITERATE PAVE. MARKING LINE, 12" WIDE & UNDER            | LF   | 30.00    | \$5.50      | \$165.00    | \$4.50      | \$135.00    |
| 641      | LOAM   | CY   | 10.00    | \$100.00    | \$1,000.00  | \$65.00     | \$650.00    |

| Item No: | Description  | Unit | Quantity | A           |              | B           |              | Total | Unit Price | Total |
|----------|--|------|----------|-------------|--------------|-------------|--------------|-------|------------|-------|
|          |  |      |          | Unit Price  | Total        | Unit Price  | Total        |       |            |       |
| 646.31   | TURF ESTABLISHMENT WITH MULCH AND TACKIFIERS         | SY   | 80.00    | \$3.75      | \$300.00     | \$25.00     | \$2,000.00   |       |            |       |
| 692      | MOBILIZATION   | U    | 1.00     | \$26,000.00 | \$26,000.00  | \$63,000.00 | \$63,000.00  |       |            |       |
| 699      | MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL | \$   | 1,000.00 | \$1.00      | \$1,000.00   | \$1.00      | \$1,000.00   |       |            |       |
|          |  |      |          |             | \$169,865.50 |             | \$199,159.00 |       |            |       |

# A - PS&E Comparison

PS&E = NHDOT Cost Estimate

| Item No: | Description                             | Unit | Quantity | A-Bidder   |             | PS&E       |             | A-PS&E Difference |
|----------|---|------|----------|------------|-------------|------------|-------------|-------------------|
|          |   |      |          | Unit Price | Total       | Unit Price | Total       |                   |
| 203.1    | COMMON EXCAVATION                       | CY   | 25.00    | \$60.00    | \$1,500.00  | \$20.00    | \$500.00    | \$1,000.00        |
| 203.2    | ROCK EXCAVATION                         | CY   | 9.00     | \$150.00   | \$1,350.00  | \$50.00    | \$450.00    | \$900.00          |
| 203.6    | EMBANKMENT-IN-PLACE (F)                 | CY   | 10.00    | \$45.00    | \$450.00    | \$30.00    | \$300.00    | \$150.00          |
| 206.19   | COMMON STRUCTURE EXCAVATION EXPLORATORY | CY   | 5.00     | \$75.00    | \$375.00    | \$50.00    | \$250.00    | \$125.00          |
| 214      | FINE GRADING                            | U    | 1.00     | \$1,800.00 | \$1,800.00  | \$1,000.00 | \$1,000.00  | \$800.00          |
| 304.301  | CRUSHED GRAVEL                          | CY   | 25.00    | \$95.00    | \$2,375.00  | \$40.00    | \$1,000.00  | \$1,375.00        |
| 304.32   | CRUSHED GRAVEL FOR SHOULDER LEVELING    | TON  | 25.00    | \$95.00    | \$2,375.00  | \$40.00    | \$1,000.00  | \$1,375.00        |
| 403.11   | HOT BITUMINOUS PAVEMENT, MACHINE METHOD | TON  | 240.00   | \$160.00   | \$38,400.00 | \$200.00   | \$48,000.00 | (\$9,600.00)      |
| 403.12   | HOT BITUMINOUS PAVEMENT, HAND METHOD    | TON  | 10.00    | \$165.00   | \$1,650.00  | \$250.00   | \$2,500.00  | (\$850.00)        |
| 403.6    | PAVEMENT JOINT ADHESIVE                 | LF   | 2,220.00 | \$2.30     | \$5,106.00  | \$1.00     | \$2,220.00  | \$2,886.00        |
| 417      | COLD PLANING BITUMINOUS SURFACES        | SY   | 210.00   | \$32.00    | \$6,720.00  | \$10.00    | \$2,100.00  | \$4,620.00        |
| 604.51   | RECONSTRUCTING/ADJUSTING SEWER MANHOLES | LF   | 1.00     | \$750.00   | \$750.00    | \$400.00   | \$400.00    | \$350.00          |
| 608.12   | 2" BITUMINOUS SIDEWALK (F)              | SY   | 25.00    | \$53.00    | \$1,325.00  | \$30.00    | \$750.00    | \$575.00          |
| 608.24   | 4" CONCRETE SIDEWALK (F)                | SY   | 35.00    | \$65.00    | \$2,275.00  | \$40.00    | \$1,400.00  | \$875.00          |
| 608.26   | 6" CONCRETE SIDEWALK (F)                | SY   | 30.00    | \$70.00    | \$2,100.00  | \$50.00    | \$1,500.00  | \$600.00          |
| 608.54   | DETECTABLE WARNING DEVICES, CAST IRON   | SY   | 8.00     | \$450.00   | \$3,600.00  | \$350.00   | \$2,800.00  | \$800.00          |
| 609.01   | STRAIGHT GRANITE CURB                   | LF   | 15.00    | \$42.00    | \$630.00    | \$25.00    | \$375.00    | \$255.00          |
| 609.216  | STRAIGHT GRANITE SLOPE CURB 6" HIGH     | LF   | 95.00    | \$40.00    | \$3,800.00  | \$25.00    | \$2,375.00  | \$1,425.00        |
| 609.236  | CURVED GRANITE SLOPE CURB 6" HIGH       | LF   | 25.00    | \$105.00   | \$2,625.00  | \$65.00    | \$1,625.00  | \$1,000.00        |
| 609.5    | RESET GRANITE CURB                      | LF   | 39.00    | \$24.00    | \$936.00    | \$20.00    | \$780.00    | \$156.00          |

## A - PS&amp;E Comparison

| Item No: | Description  | Unit | A-Bidder |             | PS&E        |             | A-PS&E Difference |              |
|----------|--|------|----------|-------------|-------------|-------------|-------------------|--------------|
|          |  |      | Quantity | Unit Price  | Total       | Unit Price  |                   | Total        |
| 615.03   | TRAFFIC SIGN TYPE C (F)                                    | SF   | 42.00    | \$66.00     | \$2,772.00  | \$55.00     | \$2,310.00        | \$462.00     |
| 615.06   | TRAFFIC SIGN TYPE CC (F)                                   | SF   | 14.00    | \$22.00     | \$308.00    | \$25.00     | \$350.00          | (\$42.00)    |
| 616.261  | RECTANGULAR RAPID FLASHING BEACON                          | U    | 1.00     | \$21,000.00 | \$21,000.00 | \$20,000.00 | \$20,000.00       | \$1,000.00   |
| 618.7    | FLAGGERS   | HR   | 240.00   | \$35.00     | \$8,400.00  | \$22.00     | \$5,280.00        | \$3,120.00   |
| 619.1    | MAINTENANCE OF TRAFFIC                                     | U    | 1.00     | \$15,000.00 | \$15,000.00 | \$20,000.00 | \$20,000.00       | (\$5,000.00) |
| 619.25   | PORTABLE CHANGEABLE MESSAGE SIGN                           | U    | 2.00     | \$4,000.00  | \$8,000.00  | \$2,500.00  | \$5,000.00        | \$3,000.00   |
| 621.31   | SINGLE DELINEATOR WITH POST                                | EA   | 3.00     | \$85.00     | \$255.00    | \$35.00     | \$105.00          | \$150.00     |
| 628.1    | SAWED CONCRETE PAVEMENT                                    | LF   | 122.00   | \$6.00      | \$732.00    | \$5.00      | \$610.00          | \$122.00     |
| 628.2    | SAWED BITUMINOUS PAVEMENT                                  | LF   | 80.00    | \$3.00      | \$240.00    | \$5.00      | \$400.00          | (\$160.00)   |
| 632.0104 | RETROREFLECTIVE PAINT PAVE. MARKING, 4" LINE               | LF   | 9,400.00 | \$0.30      | \$2,820.00  | \$0.20      | \$1,880.00        | \$940.00     |
| 632.0112 | RETROREFLECTIVE PAINT PAVE. MARKING, 12" LINE              | LF   | 125.00   | \$1.40      | \$175.00    | \$0.60      | \$75.00           | \$100.00     |
| 632.3104 | RETROREFLECT. THERMOPLAS. PAVE. MARKING, 4" LINE           | LF   | 105.00   | \$3.30      | \$346.50    | \$2.00      | \$210.00          | \$136.50     |
| 632.3112 | RETROREFLECT. THERMOPLAS. PAVE. MARKING, 12" LINE          | LF   | 70.00    | \$5.50      | \$385.00    | \$4.00      | \$280.00          | \$105.00     |
| 632.3118 | RETROREFLECT. THERMOPLAS. PAVE. MARKING, 18" LINE          | LF   | 50.00    | \$7.70      | \$385.00    | \$5.00      | \$250.00          | \$135.00     |
| 632.32   | RETROREFLECT. THERMOPLAS. PAVEMENT MARKING, SYMBOL OR WORD | SF   | 40.00    | \$11.00     | \$440.00    | \$8.00      | \$320.00          | \$120.00     |
| 632.911  | OBLITERATE PAVE. MARKING LINE, 12" WIDE & UNDER            | LF   | 30.00    | \$5.50      | \$165.00    | \$2.00      | \$60.00           | \$105.00     |
| 641      | LOAM   | CY   | 10.00    | \$100.00    | \$1,000.00  | \$40.00     | \$400.00          | \$600.00     |

# A - PS&E Comparison

PS&E = NHDOT Cost Estimate

| Item No: | Description  | Unit | Quantity | A-Bidder    |              | PS&E        |              | A-PS&E Difference |
|----------|--|------|----------|-------------|--------------|-------------|--------------|-------------------|
|          |  |      |          | Unit Price  | Total        | Unit Price  | Total        |                   |
| 646.31   | TURF ESTABLISHMENT WITH MULCH AND TACKIFIERS         | SY   | 80.00    | \$3.75      | \$300.00     | \$7.00      | \$560.00     | (\$260.00)        |
| 692      | MOBILIZATION   | U    | 1.00     | \$26,000.00 | \$26,000.00  | \$10,000.00 | \$10,000.00  | \$16,000.00       |
| 699      | MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL | \$   | 1,000.00 | \$1.00      | \$1,000.00   | \$1.00      | \$1,000.00   | \$0.00            |
|          |  |      |          |             | \$169,865.50 |             | \$140,415.00 | \$29,450.50       |





DRKEYCO-01

PSMITH

## CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)

8/21/2015

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

|   |  |                                      |
|---|--|--------------------------------------|
| <b>PRODUCER</b><br>A. B. Gile, Inc.<br>PO Box 66<br>Hanover, NH 03755   | <b>CONTACT NAME:</b><br>PHONE (A/C, No, Ext): (603) 643-4540 | <b>FAX (A/C, No):</b> (603) 643-6382 |
|   | <b>E-MAIL ADDRESS:</b>                                       |                                      |
| <b>INSURED</b><br><br>State of NH - DOT<br>John O. Morton Building<br>7 Hazen Drive-P.O. Box 483<br>Concord, NH 03302 | <b>INSURER(S) AFFORDING COVERAGE</b>                         |                                      |
|   | <b>INSURER A:</b> Acadia Insurance                           | <b>NAIC #</b><br>31325               |
|   | <b>INSURER B:</b>  |                                      |
|   | <b>INSURER C:</b>  |                                      |
|   | <b>INSURER D:</b>  |                                      |
|   | <b>INSURER E:</b>  |                                      |

## COVERAGES

CERTIFICATE NUMBER:

REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

| INSR LTR | TYPE OF INSURANCE   | ADDL SUBR INSD WVD | POLICY NUMBER | POLICY EFF (MM/DD/YYYY) | POLICY EXP (MM/DD/YYYY) | LIMITS   |
|----------|---|--------------------|---------------|-------------------------|-------------------------|--|
| A        | <b>COMMERCIAL GENERAL LIABILITY</b><br><input type="checkbox"/> CLAIMS-MADE <input type="checkbox"/> OCCUR<br><input checked="" type="checkbox"/> <b>Owner's &amp; Contractor</b><br><br>GEN'L AGGREGATE LIMIT APPLIES PER:<br><input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PROJECT <input type="checkbox"/> LOC<br>OTHER: |                    | OCP 5222132   | 08/14/2015              | 08/14/2016              | EACH OCCURRENCE \$ 2,000,000<br>DAMAGE TO RENTED PREMISES (Ea occurrence) \$<br>MED EXP (Any one person) \$<br>PERSONAL & ADV INJURY \$<br>GENERAL AGGREGATE \$ 3,000,000<br>PRODUCTS - COMP/OP AGG \$<br>\$ |
|          | <b>AUTOMOBILE LIABILITY</b><br><input type="checkbox"/> ANY AUTO<br><input type="checkbox"/> ALL OWNED AUTOS<br><input type="checkbox"/> HIRED AUTOS<br><input type="checkbox"/> SCHEDULED AUTOS<br><input type="checkbox"/> NON-OWNED AUTOS  |                    |               |                         |                         | COMBINED SINGLE LIMIT (Ea accident) \$<br>BODILY INJURY (Per person) \$<br>BODILY INJURY (Per accident) \$<br>PROPERTY DAMAGE (Per accident) \$<br>\$  |
|          | <input type="checkbox"/> <b>UMBRELLA LIAB</b> <input type="checkbox"/> OCCUR<br><input type="checkbox"/> <b>EXCESS LIAB</b> <input type="checkbox"/> CLAIMS-MADE<br>DED RETENTION \$  |                    |               |                         |                         | EACH OCCURRENCE \$<br>AGGREGATE \$<br>\$   |
|          | <b>WORKERS COMPENSATION AND EMPLOYERS' LIABILITY</b><br>ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) <input type="checkbox"/> Y <input type="checkbox"/> N <input type="checkbox"/> N/A<br>If yes, describe under DESCRIPTION OF OPERATIONS below  |                    |               |                         |                         | PER STATUTE OTH-ER<br>E.L. EACH ACCIDENT \$<br>E.L. DISEASE - EA EMPLOYEE \$<br>E.L. DISEASE - POLICY LIMIT \$   |

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)  
OCP Class 16291 - CONTRACTORS; PEDESTRIAN SAFETY IMPROVEMENTS IN LEBANON, NH; AT THE INTERSECTION OF NH ROUTE 10; OAK RIDGE ROAD AND GOULD ROAD, LEBANON NH 03766

## CERTIFICATE HOLDER

## CANCELLATION

|   |  |
|---|--|
| State of NH - DOT<br>John O. Morton Building<br>7 Hazen Drive - P.O. Box 483<br>Concord, NH 03302 | SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.<br><br><b>AUTHORIZED REPRESENTATIVE</b><br> |
|---|--|

© 1988-2014 ACORD CORPORATION. All rights reserved.
