

lam



THE STATE OF NEW HAMPSHIRE DEPARTMENT OF TRANSPORTATION



74E

William Cass, P.E. Commissioner

David Rodrigue, P.E. Assistant Commissioner

Andre Briere, Colonel, USAF (RET) Deputy Commissioner

His Excellency, Governor Christopher T. Sununu and the Honorable Council State House Concord, New Hampshire 03301

Bureau of Construction April 27, 2023

REQUESTED ACTION

1. Authorize the Department of Transportation to enter into a contract with J.P. Sicard, Inc. (Vendor 227157) of Barton, VT, on the basis of a sole bid of \$9,922,107 for widening and rehabilitation of NH 16, from the Dummer-Cambridge town line near MM 134.5, toward Errol ending before MM 135.9 (Project: Dummer-Cambridge-Errol #16304B), from the date of Governor and Council approval through September 26, 2025, unless amended by the Department in accordance with the Standard Specifications. 100% Federal Funds.

Funding is available in State Fiscal Year 2023, and is anticipated to be available in Fiscal Years 2024, 2025 and 2026 as follows, with the ability to adjust encumbrances through the Budget Office between State Fiscal Years if needed and justified:

Table with 5 columns: Funding description, FY 2023, FY 2024, FY 2025, FY 2026. Rows include Consolidated Federal Aid and Highway Contract Payments.

2. Further authorize that a contingency in the amount of \$694,547.49 be approved for payment of latent conditions, which may appear during the construction of the project. The contingency requested is 7% of the contract amount.

Table with 2 columns: Funding description, FY 2026. Row includes Highway Contract Payments for \$694,547.49.

EXPLANATION

This project is part of the State's Ten-Year Transportation Improvement Plan. This project runs northerly along NH 16 and adjacent to the Androscoggin River starting just beyond the Dummer-Cambridge town line near Mile Marker 134.5 continuing towards Errol and ending shortly before Mile Marker 135.9; approximately 6,700 feet. This includes realigning 6,300 feet of NH 16 west of the existing roadway (away from the Androscoggin River) with two 11-foot travel lanes, with 4-foot shoulders.

NH 16 is in poor condition and frequently suffers from frost heaving that impedes winter maintenance activities while also requiring slope stabilization along the Androscoggin to maintain the integrity of the existing roadway in its current location.

Page 2

The purpose of the project is to address the poor condition of the pavement and road base and to provide a sustainable roadway that maintains the connectivity of the corridor in order to minimize long-term maintenance and risk resulting from the proximity of the Androscoggin River, while preserving the scenic quality of the surrounding area.

The proposed contingency amount is 7% of the contract amount. This is to account for the risks associated with the unknown extent of existing muck and unsuitable materials, as well as the uncertainty of the clearing schedule due to the recent change to the Northern Long Eared Bat restrictions.

Although the bid costs exceeded the Department's estimate by 10.30%, the sole bid received is felt to be reasonable for the work involved. There was one item 692. Mobilization (\$950,925 over estimate) that primarily contributed to the increased cost. This amount was considered reasonable based upon the remote project location, the distance the contractor would have to travel (66 miles), and the large amount of pre-order material (2 large precast box culverts) that is required on the project. Re-advertising this project would result, in our opinion, in higher prices and prevent the completion of the work in a timely manner. The Department considers it to be in the best interest of the State to accept this bid to accomplish these needed repairs.

The Contractor has been prequalified by this Department. The Contract has been approved by the Attorney General as to form and execution, and the Department has certified that the necessary funds are available and the bid reasonably conforms to the engineer's estimate in accordance with State procedure. Copies of the fully executed contract are on file at the Secretary of State's Office and the Department of Administrative Service's Office, and subsequent to Governor and Council approval will be on file at the Department of Transportation.

This project funding is: 80% Federal funds (PROTECT (60%) and Federal Aid-Highway (40%)), with anticipated utilization of Turnpike Toll Credits for the State's 20% match, effectively using 100% Federal Funds.

A copy of the Tabulation of Bids received for this project is attached along with the Contract Supplemental Sheet and a map indicating the location of the project.

Your approval of this resolution is respectfully requested.

Sincerely,



William Cass  
Commissioner

WC/pcj

Department Estimate:	\$8,995,844.50
Contract Amount:	<u>\$9,922,107.00</u>
Over Estimate:	\$ 926,262.50
Attachments	



# ABC Bid Data

DUMMER - CAMBRIDGE - ERROL

16304B

X-A004(699)

---

PROJECT: DUMMER - CAMBRIDGE - ERROL  
STATE PROJECT NUMBER: 16304B  
FED. PROJECT NUMBER: X-A004(699)  
DATE BIDS OPEN: April 20, 2023, 2:00  
SCOPE OF WORK: Widen & rehab ~ 1.4m North of NH16 in Cambridge. From Dummer T/L to Cambridge. Amount: \$9,922,107.00  
COMPLETION DATE: September 26, 2025  
LOCATION: District 1, Coos

Awarded To: SICARD INC, J P  
234 GLOVER ROAD  
BARTON, VT 05822

Certified by: WILLIAM J. OLDENBURG  
Director of Project Development

Award Date:

## Summary of Bidders

Contractor	Bid Amount	Rank
SICARD INC, J P 234 GLOVER ROAD, BARTON VT 05822	\$9,922,107.00	A

# ABC Bid Data

DUMMER - CAMBRIDGE - ERROL

16304B

X-A004(699)

Item No.	Description	Unit	Quantity	PS&E		SICARD INC. J P 234 GLOVER ROAD BARTON, VT 05822		Unit Price	Total
				Unit Price	Total	Unit Price	Total		

Items

201.01	CLEARING (F)	A	.50	\$7,500.00	\$3,750.00	\$11,500.00	\$5,750.00		
201.1	CLEARING AND GRUBBING (F)	A	9.00	\$9,000.00	\$81,000.00	\$20,000.00	\$180,000.00		
201.682	INVASIVE SPECIES CONTROL TYPE II	SY	5.00	\$100.00	\$500.00	\$100.00	\$500.00		
202.41	REMOVAL OF EXISTING PIPE 6-24" DIAMETER	LF	360.00	\$20.00	\$7,200.00	\$27.00	\$9,720.00		
203.1	COMMON EXCAVATION	CY	52,000.00	\$12.00	\$624,000.00	\$13.00	\$676,000.00		
203.11	COMMON EXCAVATION - LRS	CY	4,250.00	\$20.00	\$85,000.00	\$13.00	\$55,250.00		
203.4	MUCK EXCAVATION	CY	7,100.00	\$18.50	\$131,350.00	\$13.50	\$95,850.00		
203.601	EMBANKMENT-IN-PLACE	CY	13,600.00	\$13.00	\$176,800.00	\$25.00	\$340,000.00		
203.661	GRAVEL BACKFILL FOR MUCK AND UNSUITABLE MATERIAL EXCAVATION	CY	12,200.00	\$35.00	\$427,000.00	\$32.00	\$390,400.00		
203.662	ROCK AND GRAVEL BACKFILL FOR MUCK AND UNSUITABLE MATERIAL EXCAVATION	CY	37,000.00	\$52.00	\$1,924,000.00	\$32.00	\$1,184,000.00		
206.1	COMMON STRUCTURE EXCAVATION	CY	1,200.00	\$40.00	\$48,000.00	\$39.00	\$46,800.00		
214.	FINE GRADING	U	1.00	\$25,000.00	\$25,000.00	\$28,000.00	\$28,000.00		
304.1	SAND (F)	CY	2,500.00	\$25.00	\$62,500.00	\$40.00	\$100,000.00		
304.2	GRAVEL (F)	CY	28,000.00	\$40.00	\$1,120,000.00	\$38.00	\$1,064,000.00		
304.3	CRUSHED GRAVEL (F)	CY	10,200.00	\$32.00	\$326,400.00	\$42.00	\$428,400.00		
304.35	CRUSHED GRAVEL FOR DRIVES	CY	120.00	\$47.00	\$5,640.00	\$52.00	\$6,240.00		
403.11031	HBP-3/4" WINTER BINDER MIX, MACHINE METHOD, QC/QA TIER 1	TON	3,850.00	\$100.00	\$385,000.00	\$111.00	\$427,350.00		
403.11041	HBP-1/2" SURFACE MIX, MACHINE METHOD, QC/QA TIER 1	TON	1,950.00	\$120.00	\$234,000.00	\$126.00	\$245,700.00		
403.12	HBP-HAND METHOD	TON	15.00	\$180.00	\$2,700.00	\$600.00	\$9,000.00		
403.16	PAVEMENT JOINT ADHESIVE	LF	16,250.00	\$0.32	\$5,200.00	\$1.00	\$16,250.00		
403.19	HBP-TEMPORARY	TON	250.00	\$100.00	\$25,000.00	\$260.00	\$65,000.00		
403.4	MATERIAL TRANSFER VEHICLE (MTV)	TON	5,800.00	\$2.85	\$16,530.00	\$4.00	\$23,200.00		
410.22	ASPHALT EMULSION FOR TACK COAT	GAL	690.00	\$4.00	\$2,760.00	\$13.00	\$8,970.00		
417.	COLD PLANING BITUMINOUS SURFACES	SY	150.00	\$20.00	\$3,000.00	\$29.00	\$4,350.00		

# ABC Bid Data

DUMMER - CAMBRIDGE - ERROL

16304B

X-A004(699)

Item No.	Description	Unit	Quantity	PS&E		SICARD INC. J P 224 GLOVER ROAD BARTON, VT 05822		Unit Price	Total
				Unit Price	Total	Unit Price	Total		
503.101	WATER DIVERSION STRUCTURE	U	1.00	\$31,000.00	\$31,000.00	\$18,140.00	\$18,140.00		
503.102	WATER DIVERSION STRUCTURE	U	1.00	\$35,000.00	\$35,000.00	\$52,250.00	\$52,250.00		
503.201	COFFERDAMS	U	1.00	\$100,000.00	\$100,000.00	\$500.00	\$500.00		
503.202	COFFERDAMS	U	1.00	\$100,000.00	\$100,000.00	\$191,500.00	\$191,500.00		
520.1	CONCRETE CLASS A	CY	30.00	\$1,000.00	\$30,000.00	\$1,995.00	\$59,850.00		
529.00101	PRECAST CONCRETE BOX CULVERT	U	1.00	\$164,000.00	\$164,000.00	\$141,350.00	\$141,350.00		
529.00102	PRECAST CONCRETE BOX CULVERT	U	1.00	\$216,000.00	\$216,000.00	\$182,300.00	\$182,300.00		
544.1	REINFORCING STEEL (ROADWAY)	LB	220.00	\$4.00	\$880.00	\$3.00	\$660.00		
585.2	STONE FILL, CLASS B	CY	370.00	\$95.00	\$35,150.00	\$52.00	\$19,240.00		
585.3	STONE FILL, CLASS C	CY	180.00	\$56.00	\$8,960.00	\$56.00	\$8,960.00		
585.3401	SIMULATED STREAMBED MATERIAL	CY	100.00	\$70.00	\$7,000.00	\$86.00	\$8,600.00		
593.221	GEOTEXTILE; SEPARATION CL.2, NON-WOVEN	SY	650.00	\$3.00	\$1,950.00	\$3.00	\$1,950.00		
593.312	GEOTEXTILE; STABILIZATION CL. 1, MONOFILAMENT, WOVEN	SY	38,000.00	\$3.00	\$114,000.00	\$2.00	\$76,000.00		
593.321	GEOTEXTILE; STABILIZATION CL.2, NON-WOVEN	SY	900.00	\$4.50	\$4,050.00	\$2.00	\$1,800.00		
593.411	GEOTEXTILE; PERM CONTROL CL.1, NON-WOVEN	SY	635.00	\$5.00	\$3,175.00	\$3.00	\$1,905.00		
603.0001	VIDEO INSPECTION	LF	1,570.00	\$5.00	\$7,850.00	\$2.00	\$3,140.00		
603.00215	15" R.C. PIPE, 2000D	LF	96.00	\$150.00	\$14,400.00	\$113.00	\$10,848.00		
603.00218	18" R.C. PIPE, 2000D	LF	200.00	\$105.00	\$21,000.00	\$153.00	\$30,600.00		
603.00224	24" R.C. PIPE, 2000D	LF	96.00	\$140.00	\$13,440.00	\$172.00	\$16,512.00		
603.00318	18" R.C. PIPE, 3000D	LF	120.00	\$168.00	\$20,160.00	\$152.00	\$18,240.00		
603.00324	24" R.C. PIPE, 3000D	LF	120.00	\$200.00	\$24,000.00	\$179.00	\$21,480.00		
603.00342	42" R.C. PIPE, 3000D	LF	68.00	\$250.00	\$17,000.00	\$260.00	\$17,680.00		
603.30115	15" R.C. END SECTIONS	EA	2.00	\$900.00	\$1,800.00	\$911.00	\$1,822.00		
603.30124	24" R.C. END SECTIONS	EA	4.00	\$1,200.00	\$4,800.00	\$1,199.00	\$4,796.00		
604.0007	POLYETHYLENE LINER	EA	11.00	\$180.00	\$1,980.00	\$315.00	\$3,465.00		
604.124	CATCH BASINS TYPE B, 4-FOOT DIAMETER	U	9.50	\$2,650.00	\$25,175.00	\$6,690.00	\$63,555.00		

Item No.	Description	Unit	Quantity	PS&E		SICARD INC. J P 234 GLOVER ROAD BARTON, VT 05822		Unit Price	Total
				Unit Price	Total	Unit Price	Total		
604.154	CATCH BASINS TYPE E, 4-FOOT DIAMETER	U	2.00	\$3,400.00	\$6,800.00	\$6,740.00	\$13,480.00		
604.1941	SPECIAL CATCH BASIN TYPE G, 4 FT DIAMETER	U	2.00	\$3,600.00	\$7,200.00	\$7,445.00	\$14,890.00		
605.506	6" PERF. CORR. POLYETHYLENE PIPE UNDERDRAIN	LF	1,640.00	\$36.00	\$59,040.00	\$32.00	\$52,480.00		
605.79	UNDERDRAIN FLUSHING BASINS	EA	5.00	\$580.00	\$2,900.00	\$770.00	\$3,850.00		
605.82552	48" AGGREGATE UNDERDRAIN TYPE 2, WITH 12" PERF. CORR. POLYETHYLENE PIPE	LF	880.00	\$95.00	\$83,600.00	\$71.00	\$62,480.00		
606.417	PORTABLE CONCRETE BARRIER FOR TRAFFIC CONTROL	LF	675.00	\$40.00	\$27,000.00	\$62.00	\$41,850.00		
615.0301	TRAFFIC SIGN TYPE C	SF	54.25	\$50.00	\$2,712.50	\$196.00	\$10,633.00		
615.033	REMOVING TRAFFIC SIGN, TYPE C	U	14.00	\$70.00	\$980.00	\$98.00	\$1,372.00		
615.0601	TRAFFIC SIGN TYPE CC	SF	5.00	\$30.00	\$150.00	\$40.00	\$200.00		
618.81	UNIFORMED OFFICERS WITH VEHICLE	\$	7,500.00	\$1.00	\$7,500.00	\$1.00	\$7,500.00		
618.7	FLAGGERS	HR	5,500.00	\$45.00	\$247,500.00	\$53.00	\$291,500.00		
619.1	MAINTENANCE OF TRAFFIC	U	1.00	\$150,000.00	\$150,000.00	\$264,856.00	\$264,856.00		
619.25	PORTABLE CHANGEABLE MESSAGE SIGN	U	2.00	\$4,600.00	\$9,200.00	\$10,265.00	\$20,530.00		
619.279	AUTOMATED TRAILER-MOUNTED SPEED LIMIT SIGN	U	2.00	\$3,500.00	\$7,000.00	\$10,265.00	\$20,530.00		
621.31	SINGLE DELINEATOR WITH POST	EA	32.00	\$55.00	\$1,760.00	\$98.00	\$3,136.00		
622.1	STEEL WITNESS MARKERS	EA	24.00	\$38.00	\$912.00	\$52.00	\$1,248.00		
622.2	CONCRETE BOUNDS	EA	12.00	\$340.00	\$4,080.00	\$460.00	\$5,520.00		
628.2	SAWED BITUMINOUS PAVEMENT	LF	210.00	\$5.00	\$1,050.00	\$4.00	\$840.00		
632.0104	RETROREFLECTIVE PAINT PAVE. MARKING, 4" LINE	LF	108,000.00	\$0.25	\$27,000.00	\$0.18	\$19,440.00		
632.911	OBLITERATE PAVE. MARKING LINE, 12" WIDE & UNDER	LF	10,000.00	\$1.00	\$10,000.00	\$0.74	\$7,400.00		
634.	BOULDERS FOR BARRICADE	EA	19.00	\$100.00	\$1,900.00	\$82.00	\$1,558.00		
645.3	EROSION STONE	TON	500.00	\$30.00	\$15,000.00	\$32.00	\$16,000.00		
645.42	TEMPORARY SLOPE MATTING TYPE B (WILDLIFE FRIENDLY)	SY	58,500.00	\$2.50	\$146,250.00	\$4.00	\$234,000.00		
645.512	COMPOST SOCK FOR PERIMETER BERM	LF	18,500.00	\$5.00	\$92,500.00	\$6.00	\$111,000.00		
645.531	SILT FENCE	LF	18,500.00	\$3.00	\$55,500.00	\$3.00	\$55,500.00		
645.811	BONDED FIBER MATRIX (BFM)	LB	600.00	\$30.00	\$18,000.00	\$2.25	\$1,350.00		

# ABC Bid Data

DUMMER - CAMBRIDGE - ERROL

16304B

X-A004(699)

Item No.	Description	Unit	Quantity	PS&E		BICARD INC. J.P. 234 GLOVER ROAD BARTON, VT 05822		Unit Price	Total
				Unit Price	Total	Unit Price	Total		
645.7	STORM WATER POLLUTION PREVENTION PLAN	U	1.00	\$6,500.00	\$6,500.00	\$4,600.00	\$4,600.00		
645.71	MONITORING SWPPP AND EROSION AND SEDIMENT CONTROLS	HR	528.00	\$100.00	\$52,800.00	\$225.00	\$118,800.00		
645.72	FINAL WETLAND IMPACT REPORT	U	1.00	\$5,000.00	\$5,000.00	\$3,450.00	\$3,450.00		
646.222	TURF ESTABLISHMENT WITHOUT MULCH (WETLAND SEED)	A	2.50	\$2,000.00	\$5,000.00	\$5,200.00	\$13,000.00		
646.31	TURF ESTABLISHMENT WITH MULCH AND TACKIFIERS	SY	1,400.00	\$6.00	\$8,400.00	\$2.00	\$2,800.00		
646.3131	TURF ESTABLISHMENT WITH MULCH AND TACKIFIERS (SHORELAND ZONE I)	SY	5,000.00	\$3.00	\$15,000.00	\$1.50	\$7,500.00		
646.3132	TURF ESTABLISHMENT WITH MULCH AND TACKIFIERS (SHORELAND ZONE II)	SY	41,500.00	\$3.00	\$124,500.00	\$1.00	\$41,500.00		
647.1	HUMUS	CY	3,750.00	\$23.00	\$86,250.00	\$26.00	\$97,500.00		
647.16	HUMUS, 6" DEEP	CY	3,580.00	\$36.00	\$128,160.00	\$26.00	\$92,560.00		
650.2	LANDSCAPING	U	1.00	\$20,000.00	\$20,000.00	\$25,000.00	\$25,000.00		
670.04601	CONSTRUCT AND REMOVE TEMPORARY WIDENING	U	1.00	\$10,000.00	\$10,000.00	\$28,238.00	\$28,238.00		
670.04602	CONSTRUCT AND REMOVE TEMPORARY WIDENING	U	1.00	\$10,000.00	\$10,000.00	\$39,838.00	\$39,838.00		
670.04603	CONSTRUCT AND REMOVE TEMPORARY WIDENING	U	1.00	\$5,000.00	\$5,000.00	\$8,545.00	\$8,545.00		
670.104	TEMPORARY PORTABLE LIGHTING	U	1.00	\$4,000.00	\$4,000.00	\$39,505.00	\$39,505.00		
670.822	GNSS CONSTRUCTION INSPECTION EQUIPMENT	U	1.00	\$25,000.00	\$25,000.00	\$38,900.00	\$38,900.00		
692.	MOBILIZATION	U	1.00	\$500,000.00	\$500,000.00	\$1,450,925.00	\$1,450,925.00		
693.	ON-THE-JOB TRAINING OF UNSKILLED WORKERS	\$	600.00	\$1.00	\$600.00	\$1.00	\$600.00		
697.11	INVASIVE SPECIES CONTROL AND MANAGEMENT PLAN	U	1.00	\$500.00	\$500.00	\$1,380.00	\$1,380.00		
697.31	PROJECT OPERATIONS PLAN	U	1.00	\$3,000.00	\$3,000.00	\$2,070.00	\$2,070.00		
698.12	FIELD OFFICE TYPE B	MON	29.00	\$2,500.00	\$72,500.00	\$2,750.00	\$79,750.00		
698.2	PHYSICAL TESTING LABORATORY	MON	27.00	\$1,000.00	\$27,000.00	\$690.00	\$18,630.00		
699.	MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00		
1008.8	ALTERATIONS AND ADDITIONS AS NEEDED - WINTER MAINTENANCE	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00		
1010.15	FUEL ADJUSTMENT	\$	70,000.00	\$1.00	\$70,000.00	\$1.00	\$70,000.00		
1010.2	ASPHALT CEMENT ADJUSTMENT	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00		

# ABC Bid Data

DUMMER - CAMBRIDGE - ERROL

16304B

X-A004(699)

Item No.	Description	Unit	Quantity	PS&E		SICARD INC. J P 234 GLOVER ROAD BARTON, VT 05622		Unit Price	Total
				Unit Price	Total	Unit Price	Total		
1010.3	QUALITY CONTROL QUALITY ASSURANCE (QC/QA) ASPHALT	\$	31,000.00	\$1.00	\$31,000.00	\$1.00	\$31,000.00		
<b>Totals:</b>					<b>\$8,995,844.50</b>		<b>\$9,922,107.00</b>		
<b>Alt. Totals:</b>									
<b>Totals:</b>					<b>\$8,995,844.50</b>		<b>\$9,922,107.00</b>		



# PS&E Comparison

DUMMER - CAMBRIDGE - ERROL

16304B

X-A004(699)

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
<b>Items</b>								
201.01	CLEARING (F)	A	.50	\$11,500.00	\$5,750.00	\$7,500.00	\$3,750.00	\$2,000.00
201.1	CLEARING AND GRUBBING (F)	A	9.00	\$20,000.00	\$180,000.00	\$9,000.00	\$81,000.00	\$99,000.00
201.882	INVASIVE SPECIES CONTROL TYPE II	SY	5.00	\$100.00	\$500.00	\$100.00	\$500.00	\$0.00
202.41	REMOVAL OF EXISTING PIPE 0-24" DIAMETER	LF	360.00	\$27.00	\$9,720.00	\$20.00	\$7,200.00	\$2,520.00
203.1	COMMON EXCAVATION	CY	52,000.00	\$13.00	\$676,000.00	\$12.00	\$624,000.00	\$52,000.00
203.11	COMMON EXCAVATION - LRS	CY	4,250.00	\$13.00	\$55,250.00	\$20.00	\$85,000.00	(\$29,750.00)
203.4	MUCK EXCAVATION	CY	7,100.00	\$13.50	\$95,850.00	\$18.50	\$131,350.00	(\$35,500.00)
203.601	EMBANKMENT-IN-PLACE	CY	13,600.00	\$25.00	\$340,000.00	\$13.00	\$176,800.00	\$163,200.00
203.661	GRAVEL BACKFILL FOR MUCK AND UNSUITABLE MATERIAL EXCAVATION	CY	12,200.00	\$32.00	\$390,400.00	\$35.00	\$427,000.00	(\$36,600.00)
203.662	ROCK AND GRAVEL BACKFILL FOR MUCK AND UNSUITABLE MATERIAL EXCAVATION	CY	37,000.00	\$32.00	\$1,184,000.00	\$52.00	\$1,924,000.00	(\$740,000.00)
206.1	COMMON STRUCTURE EXCAVATION	CY	1,200.00	\$39.00	\$46,800.00	\$40.00	\$48,000.00	(\$1,200.00)
214.	FINE GRADING	U	1.00	\$28,000.00	\$28,000.00	\$25,000.00	\$25,000.00	\$3,000.00
304.1	SAND (F)	CY	2,500.00	\$40.00	\$100,000.00	\$25.00	\$62,500.00	\$37,500.00
304.2	GRAVEL (F)	CY	28,000.00	\$38.00	\$1,064,000.00	\$40.00	\$1,120,000.00	(\$56,000.00)



# PS&E Comparison

DUMMER - CAMBRIDGE - ERROL

16304B

X-A004(699)

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
304.3	CRUSHED GRAVEL (F)	CY	10,200.00	\$42.00	\$428,400.00	\$32.00	\$326,400.00	\$102,000.00
304.35	CRUSHED GRAVEL FOR DRIVES	CY	120.00	\$52.00	\$6,240.00	\$47.00	\$5,640.00	\$600.00
403.11031	HBP-3/4" WINTER BINDER MIX, MACHINE METHOD, QC/QA TIER 1	TON	3,850.00	\$111.00	\$427,350.00	\$100.00	\$385,000.00	\$42,350.00
403.11041	HBP-1/2" SURFACE MIX, MACHINE METHOD, QC/QA TIER 1	TON	1,950.00	\$126.00	\$245,700.00	\$120.00	\$234,000.00	\$11,700.00
403.12	HBP-HAND METHOD	TON	15.00	\$600.00	\$9,000.00	\$180.00	\$2,700.00	\$6,300.00
403.16	PAVEMENT JOINT ADHESIVE	LF	16,250.00	\$1.00	\$16,250.00	\$0.32	\$5,200.00	\$11,050.00
403.19	HBP-TEMPORARY	TON	250.00	\$260.00	\$65,000.00	\$100.00	\$25,000.00	\$40,000.00
403.4	MATERIAL TRANSFER VEHICLE (MTV)	TON	5,800.00	\$4.00	\$23,200.00	\$2.85	\$16,530.00	\$6,670.00
410.22	ASPHALT EMULSION FOR TACK COAT	GAL	690.00	\$13.00	\$8,970.00	\$4.00	\$2,760.00	\$6,210.00
417.	COLD PLANING BITUMINOUS SURFACES	SY	150.00	\$29.00	\$4,350.00	\$20.00	\$3,000.00	\$1,350.00
503.101	WATER DIVERSION STRUCTURE	U	1.00	\$18,140.00	\$18,140.00	\$31,000.00	\$31,000.00	(\$12,860.00)
503.102	WATER DIVERSION STRUCTURE	U	1.00	\$52,250.00	\$52,250.00	\$35,000.00	\$35,000.00	\$17,250.00
503.201	COFFERDAMS	U	1.00	\$500.00	\$500.00	\$100,000.00	\$100,000.00	(\$99,500.00)
503.202	COFFERDAMS	U	1.00	\$191,500.00	\$191,500.00	\$100,000.00	\$100,000.00	\$91,500.00
520.1	CONCRETE CLASS A	CY	30.00	\$1,995.00	\$59,850.00	\$1,000.00	\$30,000.00	\$29,850.00
529.00101	PRECAST CONCRETE BOX CULVERT	U	1.00	\$141,350.00	\$141,350.00	\$164,000.00	\$164,000.00	(\$22,650.00)

PS&E Comparison

DUMMER - CAMBRIDGE - ERROL

16304B

X-A004(699)

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
529.00102	PRECAST CONCRETE BOX CULVERT	U	1.00	\$182,300.00	\$182,300.00	\$216,000.00	\$216,000.00	(\$33,700.00)
544.1	REINFORCING STEEL (ROADWAY)	LB	220.00	\$3.00	\$660.00	\$4.00	\$880.00	(\$220.00)
585.2	STONE FILL, CLASS B	CY	370.00	\$52.00	\$19,240.00	\$95.00	\$35,150.00	(\$15,910.00)
585.3	STONE FILL, CLASS C	CY	160.00	\$56.00	\$8,960.00	\$56.00	\$8,960.00	\$0.00
585.3401	SIMULATED STREAMBED MATERIAL	CY	100.00	\$86.00	\$8,600.00	\$70.00	\$7,000.00	\$1,600.00
593.221	GEOTEXTILE; SEPARATION CL.2, NON-WOVEN	SY	650.00	\$3.00	\$1,950.00	\$3.00	\$1,950.00	\$0.00
593.312	GEOTEXTILE; STABILIZATION CL. 1, MONOFILAMENT, WOVEN	SY	38,000.00	\$2.00	\$76,000.00	\$3.00	\$114,000.00	(\$38,000.00)
593.321	GEOTEXTILE; STABILIZATION CL.2, NON-WOVEN	SY	900.00	\$2.00	\$1,800.00	\$4.50	\$4,050.00	(\$2,250.00)
593.411	GEOTEXTILE; PERM CONTROL CL.1, NON-WOVEN	SY	635.00	\$3.00	\$1,905.00	\$5.00	\$3,175.00	(\$1,270.00)
603.0001	VIDEO INSPECTION	LF	1,570.00	\$2.00	\$3,140.00	\$5.00	\$7,850.00	(\$4,710.00)
603.00215	15" R.C. PIPE, 2000D	LF	96.00	\$113.00	\$10,848.00	\$150.00	\$14,400.00	(\$3,552.00)
603.00218	18" R.C. PIPE, 2000D	LF	200.00	\$153.00	\$30,600.00	\$105.00	\$21,000.00	\$9,600.00
603.00224	24" R.C. PIPE, 2000D	LF	96.00	\$172.00	\$16,512.00	\$140.00	\$13,440.00	\$3,072.00
603.00318	18" R.C. PIPE, 3000D	LF	120.00	\$152.00	\$18,240.00	\$168.00	\$20,160.00	(\$1,920.00)
603.00324	24" R.C. PIPE, 3000D	LF	120.00	\$179.00	\$21,480.00	\$200.00	\$24,000.00	(\$2,520.00)
603.00342	42" R.C. PIPE, 3000D	LF	68.00	\$260.00	\$17,680.00	\$250.00	\$17,000.00	\$680.00
603.30115	15" R.C. END SECTIONS	EA	2.00	\$911.00	\$1,822.00	\$900.00	\$1,800.00	\$22.00

## PS&E Comparison

DUMMER - CAMBRIDGE - ERROL

16304B

X-A004(699)

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
603.30124	24" R.C. END SECTIONS	EA	4.00	\$1,199.00	\$4,796.00	\$1,200.00	\$4,800.00	(\$4.00)
604.0007	POLYETHYLENE LINER	EA	11.00	\$315.00	\$3,465.00	\$180.00	\$1,980.00	\$1,485.00
604.124	CATCH BASINS TYPE B, 4-FOOT DIAMETER	U	9.50	\$6,690.00	\$63,555.00	\$2,650.00	\$25,175.00	\$38,380.00
604.154	CATCH BASINS TYPE E, 4-FOOT DIAMETER	U	2.00	\$6,740.00	\$13,480.00	\$3,400.00	\$6,800.00	\$6,680.00
604.1941	SPECIAL CATCH BASIN TYPE G, 4 FT DIAMETER	U	2.00	\$7,445.00	\$14,890.00	\$3,600.00	\$7,200.00	\$7,690.00
605.506	6" PERF. CORR. POLYETHYLENE PIPE UNDERDRAIN	LF	1,640.00	\$32.00	\$52,480.00	\$36.00	\$59,040.00	(\$6,560.00)
605.79	UNDERDRAIN FLUSHING BASINS	EA	5.00	\$770.00	\$3,850.00	\$580.00	\$2,900.00	\$950.00
605.82552	48" AGGREGATE UNDERDRAIN TYPE 2, WITH 12" PERF. CORR. POLYETHYLENE PIPE	LF	880.00	\$71.00	\$62,480.00	\$95.00	\$83,600.00	(\$21,120.00)
606.417	PORTABLE CONCRETE BARRIER FOR TRAFFIC CONTROL	LF	675.00	\$62.00	\$41,850.00	\$40.00	\$27,000.00	\$14,850.00
615.0301	TRAFFIC SIGN TYPE C	SF	54.25	\$196.00	\$10,633.00	\$50.00	\$2,712.50	\$7,920.50
615.033	REMOVING TRAFFIC SIGN, TYPE C	U	14.00	\$98.00	\$1,372.00	\$70.00	\$980.00	\$392.00
615.0601	TRAFFIC SIGN TYPE CC	SF	5.00	\$40.00	\$200.00	\$30.00	\$150.00	\$50.00
618.61	UNIFORMED OFFICERS WITH VEHICLE	\$	7,500.00	\$1.00	\$7,500.00	\$1.00	\$7,500.00	\$0.00
618.7	FLAGGERS	HR	5,500.00	\$53.00	\$291,500.00	\$45.00	\$247,500.00	\$44,000.00
619.1	MAINTENANCE OF TRAFFIC	U	1.00	\$264,856.00	\$264,856.00	\$150,000.00	\$150,000.00	\$114,856.00
619.25	PORTABLE CHANGEABLE MESSAGE SIGN	U	2.00	\$10,265.00	\$20,530.00	\$4,600.00	\$9,200.00	\$11,330.00
619.279	AUTOMATED TRAILER-MOUNTED SPEED LIMIT SIGN	U	2.00	\$10,265.00	\$20,530.00	\$3,500.00	\$7,000.00	\$13,530.00

## PS&E Comparison

DUMMER - CAMBRIDGE - ERROL

16304B

X-A004(699)

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
621.31	SINGLE DELINEATOR WITH POST	EA	32.00	\$98.00	\$3,136.00	\$55.00	\$1,760.00	\$1,376.00
622.1	STEEL WITNESS MARKERS	EA	24.00	\$52.00	\$1,248.00	\$38.00	\$912.00	\$336.00
622.2	CONCRETE BOUNDS	EA	12.00	\$460.00	\$5,520.00	\$340.00	\$4,080.00	\$1,440.00
628.2	SAWED BITUMINOUS PAVEMENT	LF	210.00	\$4.00	\$840.00	\$5.00	\$1,050.00	(\$210.00)
632.0104	RETROREFLECTIVE PAINT PAVE. MARKING, 4" LINE	LF	108,000.00	\$0.18	\$19,440.00	\$0.25	\$27,000.00	(\$7,560.00)
632.911	OBLITERATE PAVE. MARKING LINE, 12" WIDE & UNDER	LF	10,000.00	\$0.74	\$7,400.00	\$1.00	\$10,000.00	(\$2,600.00)
634.	BOULDERS FOR BARRICADE	EA	19.00	\$82.00	\$1,558.00	\$100.00	\$1,900.00	(\$342.00)
645.3	EROSION STONE	TON	500.00	\$32.00	\$16,000.00	\$30.00	\$15,000.00	\$1,000.00
645.42	TEMPORARY SLOPE MATTING TYPE B (WILDLIFE FRIENDLY)	SY	58,500.00	\$4.00	\$234,000.00	\$2.50	\$146,250.00	\$87,750.00
645.512	COMPOST SOCK FOR PERIMETER BERM	LF	18,500.00	\$6.00	\$111,000.00	\$5.00	\$92,500.00	\$18,500.00
645.531	SILT FENCE	LF	18,500.00	\$3.00	\$55,500.00	\$3.00	\$55,500.00	\$0.00
645.611	BONDED FIBER MATRIX (BFM)	LB	600.00	\$2.25	\$1,350.00	\$30.00	\$18,000.00	(\$16,650.00)
645.7	STORM WATER POLLUTION PREVENTION PLAN	U	1.00	\$4,600.00	\$4,600.00	\$6,500.00	\$6,500.00	(\$1,900.00)
645.71	MONITORING SWPPP AND EROSION AND SEDIMENT CONTROLS	HR	528.00	\$225.00	\$118,800.00	\$100.00	\$52,800.00	\$66,000.00
645.72	FINAL WETLAND IMPACT REPORT	U	1.00	\$3,450.00	\$3,450.00	\$5,000.00	\$5,000.00	(\$1,550.00)
646.222	TURF ESTABLISHMENT WITHOUT MULCH (WETLAND SEED)	A	2.50	\$5,200.00	\$13,000.00	\$2,000.00	\$5,000.00	\$8,000.00

## PS&E Comparison

DUMMER - CAMBRIDGE - ERROL

16304B

X-A004(699)

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
646.31	TURF ESTABLISHMENT WITH MULCH AND TACKIFIERS	SY	1,400.00	\$2.00	\$2,800.00	\$6.00	\$8,400.00	(\$5,600.00)
646.3131	TURF ESTABLISHMENT WITH MULCH AND TACKIFIERS (SHORELAND ZONE I)	SY	5,000.00	\$1.50	\$7,500.00	\$3.00	\$15,000.00	(\$7,500.00)
646.3132	TURF ESTABLISHMENT WITH MULCH AND TACKIFIERS (SHORELAND ZONE II)	SY	41,500.00	\$1.00	\$41,500.00	\$3.00	\$124,500.00	(\$83,000.00)
647.1	HUMUS	CY	3,750.00	\$26.00	\$97,500.00	\$23.00	\$86,250.00	\$11,250.00
647.16	HUMUS, 6" DEEP	CY	3,560.00	\$26.00	\$92,560.00	\$36.00	\$128,160.00	(\$35,600.00)
650.2	LANDSCAPING	U	1.00	\$25,000.00	\$25,000.00	\$20,000.00	\$20,000.00	\$5,000.00
670.04601	CONSTRUCT AND REMOVE TEMPORARY WIDENING	U	1.00	\$28,238.00	\$28,238.00	\$10,000.00	\$10,000.00	\$18,238.00
670.04602	CONSTRUCT AND REMOVE TEMPORARY WIDENING	U	1.00	\$39,838.00	\$39,838.00	\$10,000.00	\$10,000.00	\$29,838.00
670.04603	CONSTRUCT AND REMOVE TEMPORARY WIDENING	U	1.00	\$8,545.00	\$8,545.00	\$5,000.00	\$5,000.00	\$3,545.00
670.104	TEMPORARY PORTABLE LIGHTING	U	1.00	\$39,505.00	\$39,505.00	\$4,000.00	\$4,000.00	\$35,505.00
670.822	GNSS CONSTRUCTION INSPECTION EQUIPMENT	U	1.00	\$38,900.00	\$38,900.00	\$25,000.00	\$25,000.00	\$13,900.00
692.	MOBILIZATION	U	1.00	\$1,450,925.00	\$1,450,925.00	\$500,000.00	\$500,000.00	\$950,925.00
693.	ON-THE-JOB TRAINING OF UNSKILLED WORKERS	\$	600.00	\$1.00	\$600.00	\$1.00	\$600.00	\$0.00
697.11	INVASIVE SPECIES CONTROL AND MANAGEMENT PLAN	U	1.00	\$1,380.00	\$1,380.00	\$500.00	\$500.00	\$880.00
697.31	PROJECT OPERATIONS PLAN	U	1.00	\$2,070.00	\$2,070.00	\$3,000.00	\$3,000.00	(\$930.00)
698.12	FIELD OFFICE TYPE B	MON	29.00	\$2,750.00	\$79,750.00	\$2,500.00	\$72,500.00	\$7,250.00



# PS&E Comparison

DUMMER - CAMBRIDGE - ERROL  
 16304B  
 X-A004(699)

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
698.2	PHYSICAL TESTING LABORATORY	MON	27.00	\$690.00	\$18,630.00	\$1,000.00	\$27,000.00	(\$8,370.00)
699.	MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00	\$0.00
1008.8	ALTERATIONS AND ADDITIONS AS NEEDED - WINTER MAINTENANCE	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00	\$0.00
1010.15	FUEL ADJUSTMENT	\$	70,000.00	\$1.00	\$70,000.00	\$1.00	\$70,000.00	\$0.00
1010.2	ASPHALT CEMENT ADJUSTMENT	\$	25,000.00	\$1.00	\$25,000.00	\$1.00	\$25,000.00	\$0.00
1010.3	QUALITY CONTROL QUALITY ASSURANCE (QC/QA) ASPHALT	\$	31,000.00	\$1.00	\$31,000.00	\$1.00	\$31,000.00	\$0.00
<b>Total:</b>					\$9,922,107.00		\$8,995,844.50	\$926,262.50

February 14, 2023

## SUPPLEMENTAL PROJECT INFORMATION SHEET

**DESCRIPTION:** This project runs northerly along NH 16 and adjacent to the Androscoggin River starting just beyond the Dummer-Cambridge town line near Mile Marker 134.5 continuing towards Errol and ending shortly before Mile Marker 135.9; approximately 6,700 feet. This includes realigning 6,300 feet of NH 16 west of the existing roadway (away from the Androscoggin River) with two 11-foot travel lanes with 4-foot shoulders.

**FEDERAL FUNDING:** 80% (PROTECT (60%) and Federal Aid-Highway (40%)) utilizing Turnpike Toll credits as the State's 20% match.

**CONTINGENCY:** The proposed contingency amount is 7% of the contract amount. This is to account for the risks associated with the unknown extent of existing muck and unsuitable materials, as well as the uncertainty of the clearing schedule due to the recent change to the Northern Long Eared Bat restrictions.

**PROJECT INITIATED:** This location was identified as priority number one within the NH 16 corridor, based on a field review from March 2013 and discussions with District 1, and subsequently identified as a Ten-Year Plan project.


**PROJECT EXPLANATION:** NH 16 is in poor condition and frequently suffers from frost heaving that impedes winter maintenance activities while also requiring slope stabilization along the Androscoggin to maintain the integrity of the existing roadway in its current location.

The purpose of the project is to address the poor condition of the pavement and road base and to provide a sustainable roadway that maintains the connectivity of the corridor in order to minimize long-term maintenance and risk resulting from the proximity of the Androscoggin River while preserving the scenic quality of the surrounding area.

**TRAFFIC IMPLICATION:** This project will be primarily constructed offline, allowing for minimal traffic interruption. Construction of the southern stream crossing is anticipated to require a lane shift with precast concrete barrier. The remaining work will require temporary widenings with one-lane, alternating two-way traffic during work hours to construct the project matches.

**COMPLETION DATE:** September 26, 2025

# DUMMER-CAMBRIDGE-ERROL - ROUTE 16

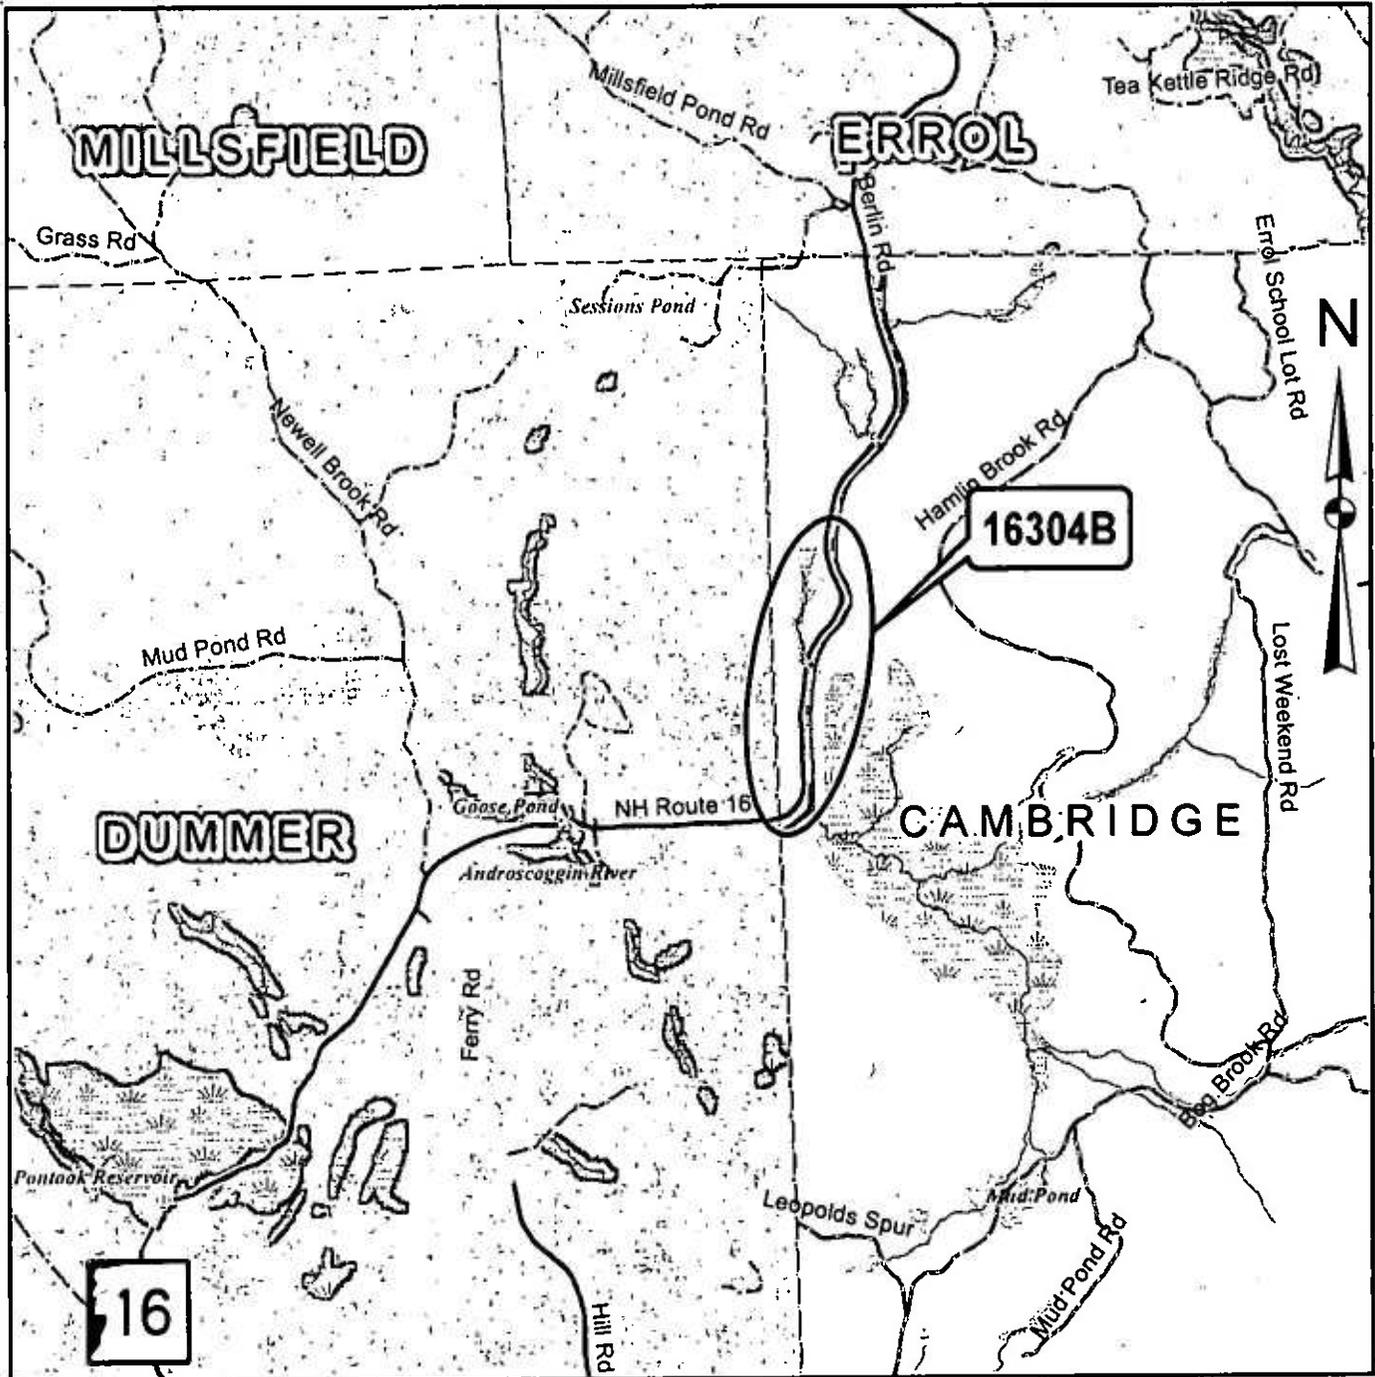


## LEGEND

- Streams
- Water Bodies
- US Routes
- State Routes
- Interstates
- Local Roads
- Town Boundary

New Hampshire  
**DOT**  
 Department of Transportation

State #: 16304B  
 Federal #: X-A004 (699)  
**LOCATION MAP**

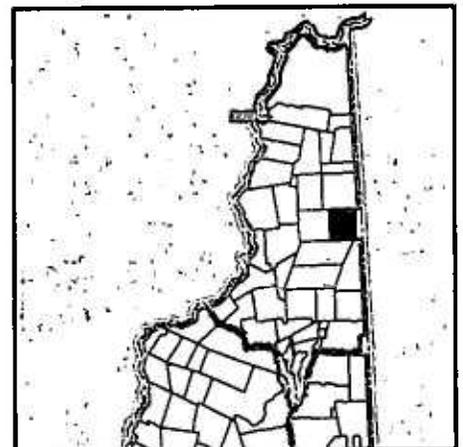

# State of New Hampshire

## Department of State

### CERTIFICATE

I, David M. Scanlan, Secretary of State of the State of New Hampshire, do hereby certify that J. P. SICARD, INC. is a Vermont Profit Corporation registered to transact business in New Hampshire on March 06, 2002. I further certify that all fees and documents required by the Secretary of State's office have been received and is in good standing as far as this office is concerned.

Business ID: 400027

Certificate Number: 0006222760



IN TESTIMONY WHEREOF,  
I hereto set my hand and cause to be affixed  
the Seal of the State of New Hampshire,  
this 4th day of May A.D. 2023.

A handwritten signature in black ink, appearing to read "D. Scanlan", is written over a faint circular stamp.

David M. Scanlan  
Secretary of State



P.O. Box 508, Barton, Vermont, 05822 • Phone: (802) 525-9506 • Fax (802) 525-4616

---

**RESOLUTION OF SOLE SHAREHOLDER IN LIEU OF**  
**2023 ANNUAL MEETING OF**  
**J. P. SICARD, INC.**

The undersigned, being the sole Shareholder of J. P. Sicard, Inc., hereby consent and agree, pursuant to 11A V.S.A. § 7.04, that the following actions may be taken forthwith and shall become effective without the necessity of calling a formal Annual Meeting of the Shareholder of the Corporation:

RESOLVED, that the following persons are authorized to bid, enter into and sign contracts for the corporation during the ensuing year and until his successor is appointed: Jason P. Sicard, Paul A. Sicard and George Carpenter.

Dated at the Town of Barton, Vermont, this, 4th day of January 2023.

This vote has not been amended or repealed and remains in full force and effect as of May 1, 2023.



---

Jason Sicard - President





# CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)  
4/27/2023

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

**IMPORTANT:** If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

<b>PRODUCER</b> Kinney Pike Insurance a One Digital Company 1011 North Main Street, Suite 4 White River Junction, VT 05001	<b>CONTACT NAME:</b> PHONE (A/C, No, Ext): (802) 775-2311		FAX (A/C, No): (802) 295-7701	
	<b>E-MAIL ADDRESS:</b>			
<b>INSURED</b> State of New Hampshire DOT PO Box 483 7 Hazen Drive Concord, NH 03301	<b>INSURER(S) AFFORDING COVERAGE</b>		<b>NAIC #</b>	
	<b>INSURER A:</b> Travelers Casualty Insurance Company of Americ		19046	
	<b>INSURER B:</b>			
	<b>INSURER C:</b>			
	<b>INSURER D:</b>			
	<b>INSURER E:</b>			
<b>INSURER F:</b>				

**COVERAGES**                      **CERTIFICATE NUMBER:**                      **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSD	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	<b>COMMERCIAL GENERAL LIABILITY</b> <input type="checkbox"/> CLAIMS-MADE <input type="checkbox"/> OCCUR <input checked="" type="checkbox"/> <b>Owner's &amp; Contractor</b>  GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC OTHER:			PRS-5R658800-IND	5/1/2023	5/1/2024	EACH OCCURRENCE \$ 2,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$ MED EXP (Any one person) \$ PERSONAL & ADV INJURY \$ GENERAL AGGREGATE \$ 3,000,000 PRODUCTS - COMP/OP AGG \$ \$
	<b>AUTOMOBILE LIABILITY</b> <input type="checkbox"/> ANY AUTO OWNED AUTOS ONLY <input type="checkbox"/> HIRED AUTOS ONLY <input type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> NON-OWNED AUTOS ONLY						COMBINED SINGLE LIMIT (Ea accident) \$ BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ \$
	<b>UMBRELLA LIAB</b> <input type="checkbox"/> OCCUR <b>EXCESS LIAB</b> <input type="checkbox"/> CLAIMS-MADE DED    RETENTION \$						EACH OCCURRENCE \$ AGGREGATE \$ \$
	<b>WORKERS COMPENSATION AND EMPLOYERS' LIABILITY</b> ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) <input type="checkbox"/> Y/N If yes, describe under DESCRIPTION OF OPERATIONS below		N/A				PER STATUTE    OTH-ER E.L. EACH ACCIDENT \$ E.L. DISEASE - EA EMPLOYEE \$ E.L. DISEASE - POLICY LIMIT \$

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)  
RE: Dummer-Cambridge-Errol X-A004(699) 16304B

**CERTIFICATE HOLDER**

**CANCELLATION**

State of New Hampshire DOT  
PO Box 483  
7 Hazen Drive  
Concord, NH 03301

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE
