

2017



THE STATE OF NEW HAMPSHIRE
DEPARTMENT OF TRANSPORTATION



28

William Cass, P.E.
Commissioner

David Rodrigue, P.E.
Assistant Commissioner
Andre Briere, Colonel, USAF (RET)
Deputy Commissioner

His Excellency, Governor Christopher T. Sununu
and the Honorable Council
State House
Concord, New Hampshire 03301

Bureau of Construction
May 11, 2023

REQUESTED ACTION

1. Authorize the Department of Transportation to enter into a contract with SUR Construction, Inc. (Vendor 156303) of Rochester, NH, on the basis of a sole bid of \$566,245, for Turnpike drainage rehabilitation on US 202 (Spaulding) Connector from Chestnut Hill Rd., to NH Rt. 125 in Rochester (Project: Turnpike Drainage #43303), from the date of Governor and Council approval through September 29, 2023, unless amended by the Department in accordance with the Standard Specifications. 100% Turnpike Funds.

Funding is anticipated to be available in State Fiscal Year 2024 as follows:

Funding is available as follows:	<u>FY 2024</u>
04-96-96-961017-7025	
Turnpike Renewal & Replacement	
400-500870 Highway Contract Payments	\$566,245

2. Further authorize that a contingency in the amount of \$28,312.25 be approved for payment of latent conditions, which may appear during the construction of the project. The contingency requested is 5% of the contract amount.

Funding is available as follows:	<u>FY 2024</u>
04-96-96-961017-7025	
Turnpike Renewal & Replacement	
400-500870 Highway Contract Payments	\$28,312.25

EXPLANATION

This project is part of the Turnpike's Renewal and Replacement Program. The project is located along the US 202 (Spaulding) Connector from Chestnut Hill Road to NH Route 125 in Rochester, with 2 specific locations. The first location is west of The Spaulding Connector near Chestnut Hill Road and the other east of the Spaulding Connector near the NH 125 overpass. On the westerly side of the project, near Chestnut Hill Road, five pipes will be slip-lined with cured in place liners; one 36" cmp under the roadway and four 15" cmps from median catch basins. In addition, the 36" cmp pipe will require repair to the MRM headwall. On the easterly side of the project, near NH Route 125, five cmp slope pipes will be replaced with plastic slope pipes.

The purpose of this project is to repair and replace ten existing metal drainage pipes along the US Route 202 Connector. These pipes are all corrugated metal which are deteriorated and are at the end of their expect life.

The proposed contingency amount is 5% of the contract amount.

Although the bid costs exceeded the Department's estimate by 38.90%, the sole bid received is felt to be reasonable for the work involved. The majority of items that were above the engineer's estimate related to the construction and removal of temporary access roads (Items 670.0491, 671.0492, and 670.0493) to access the drainage from the roadway, these items amounted to \$133,000 of the increase in cost. Re-advertising this project would result, in our opinion, in higher prices and prevent the completion of the work in a timely manner. The Department considers it to be in the best interest of the State to accept this bid to accomplish these needed repairs.

The Contractor has been prequalified by this Department. The Contract has been approved by the Attorney General as to form and execution, and the Department has certified that the necessary funds are available and the bid reasonably conforms to the engineer's estimate in accordance with State procedure. Copies of the fully executed contract are on file at the Secretary of State's Office and the Department of Administrative Service's Office, and subsequent to Governor and Council approval will be on file at the Department of Transportation.

This project funding is: 0% Federal funds (100% - Turnpike Funded from the Renewal and Replacement Program).

A copy of the Tabulation of Bids received for this project is attached along with the Contract Supplemental Sheet and a map indicating the location of the project.

Your approval of this resolution is respectfully requested.

Sincerely,



William Cass
Commissioner

WC/pcj

Department Estimate:	\$407,675
Contract Amount:	<u>\$566,245</u>
Over Estimate:	\$158,570
Attachments	



ABC Bid Data

TURNPIKE DRAINAGE

43303

NON-FEDERAL

PROJECT: TURNPIKE DRAINAGE
STATE PROJECT NUMBER: 43303
FED. PROJECT NUMBER: NON-FEDERAL
DATE BIDS OPEN: April 20, 2023, 2:00
SCOPE OF WORK: Turnpike Drainage Rehabilitation
COMPLETION DATE: September 29, 2023
LOCATION: Strafford

Awarded To: SUR CONSTRUCTION, INC.
PO BOX 720
Rochester, NH 03867

Amount: \$566,245.00
Award Date:

Certified by: WILLIAM J. OLDENBURG
Director of Project Development

Summary of Bidders

Contractor	Bid Amount	Rank
SUR CONSTRUCTION, INC. PO BOX 720 ROCHESTER NH 03867	\$566,245.00	A

Item No.	Description	Unit	Quantity	PS&E		SUR CONSTRUCTION, INC. PO BOX 720 Rochester, NH 03867		Unit Price	Total
				Unit Price	Total	Unit Price	Total		

Items

203.1	COMMON EXCAVATION	CY	10.00	\$45.00	\$450.00	\$100.00	\$1,000.00		
203.601	EMBANKMENT-IN-PLACE	CY	10.00	\$55.00	\$550.00	\$100.00	\$1,000.00		
206.19	COMMON STRUCTURE EXCAVATION EXPLORATORY	CY	10.00	\$100.00	\$1,000.00	\$100.00	\$1,000.00		
209.1	GRANULAR BACKFILL	CY	10.00	\$100.00	\$1,000.00	\$100.00	\$1,000.00		
503.1	WATER DIVERSION STRUCTURES	U	1.00	\$7,500.00	\$7,500.00	\$15,000.00	\$15,000.00		
571.1	REPAIRING AND POINTING STONE MASONRY	SY	7.00	\$400.00	\$2,800.00	\$500.00	\$3,500.00		
585.3	STONE FILL, CLASS C	CY	22.00	\$90.00	\$1,980.00	\$150.00	\$3,300.00		
593.411	GEOTEXTILE; PERM CONTROL CL.1, NON-WOVEN	SY	60.00	\$7.00	\$420.00	\$5.00	\$300.00		
602.63515	UV CURED-IN-PLACE LINER FOR 15" PIPE	LF	130.00	\$350.00	\$45,500.00	\$300.00	\$39,000.00		
602.63536	UV CURED-IN-PLACE LINER FOR 36" PIPE	LF	110.00	\$500.00	\$55,000.00	\$400.00	\$44,000.00		
603.33212	12" CORR. POLYETHYLENE END SECTION	EA	5.00	\$750.00	\$3,750.00	\$360.00	\$1,800.00		
603.40012	12" PIPE FOR SLOPE DRAINAGE	LF	190.00	\$70.00	\$13,300.00	\$170.00	\$32,300.00		
604.0007	POLYETHYLENE LINER	EA	6.00	\$200.00	\$1,200.00	\$200.00	\$1,200.00		
604.4	RECONSTRUCTING/ADJUSTING CATCH BASIN & DROP INLET	LF	4.00	\$625.00	\$2,500.00	\$1,400.00	\$5,600.00		
604.72	GRATES & FRAMES, TYPE B	EA	2.00	\$850.00	\$1,700.00	\$1,800.00	\$3,600.00		
606.91	RESETTING OR SETTING GUARDRAIL	LF	50.00	\$45.00	\$2,250.00	\$200.00	\$10,000.00		
611.05208	8" CEMENT LINED DUCTILE IRON WATER PIPE, CL 52	LF	25.00	\$120.00	\$3,000.00	\$335.00	\$8,375.00		
611.70008	8" FITTING	EA	4.00	\$650.00	\$2,600.00	\$1,800.00	\$7,200.00		
618.81	UNIFORMED OFFICERS WITH VEHICLE	\$	10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00		
618.7	FLAGGERS	HR	40.00	\$40.00	\$1,600.00	\$100.00	\$4,000.00		
619.1	MAINTENANCE OF TRAFFIC	U	1.00	\$30,000.00	\$30,000.00	\$35,000.00	\$35,000.00		
619.25	PORTABLE CHANGEABLE MESSAGE SIGN	U	2.00	-\$3,100.00	\$6,200.00	\$2,500.00	\$5,000.00		
619.83	TRUCK-MOUNTED IMPACT ATTENUATOR, TEST LEVEL 3	U	1.00	\$15,000.00	\$15,000.00	\$7,500.00	\$7,500.00		
622.1	STEEL WITNESS MARKERS	EA	9.00	\$200.00	\$1,800.00	\$100.00	\$900.00		

ABC Bid Data

TURNPIKE DRAINAGE

43303

NON-FEDERAL

Item No.	Description	Unit	Quantity	P&E		SUR CONSTRUCTION, INC. PO BOX 720 Rochester, NH 03087		Unit Price	Total
				Unit Price	Total	Unit Price	Total		
645.44	TEMPORARY SLOPE MATTING TYPE D (WILDLIFE FRIENDLY)	SY	225.00	\$5.00	\$1,125.00	\$3.00	\$675.00		
645.512	COMPOST SOCK FOR PERIMETER BERM	LF	765.00	\$8.00	\$6,120.00	\$8.00	\$6,120.00		
645.531	SILT FENCE	LF	765.00	\$4.00	\$3,060.00	\$8.00	\$6,120.00		
646.31	TURF ESTABLISHMENT WITH MULCH AND TACKIFIERS	SY	225.00	\$14.00	\$3,150.00	\$5.00	\$1,125.00		
647.1	HUMUS	CY	78.00	\$40.00	\$3,120.00	\$85.00	\$6,630.00		
670.0491	CONSTRUCT AND REMOVE TEMPORARY ACCESS ROAD	U	1.00	\$40,000.00	\$40,000.00	\$100,000.00	\$100,000.00		
670.0492	CONSTRUCT AND REMOVE TEMPORARY ACCESS ROAD	U	1.00	\$10,000.00	\$10,000.00	\$33,000.00	\$33,000.00		
670.0493	CONSTRUCT AND REMOVE TEMPORARY ACCESS ROAD	U	1.00	\$10,000.00	\$10,000.00	\$33,000.00	\$33,000.00		
670.313	PIPE CLEAN OUT AND DEBRIS REMOVAL	U	3.00	\$6,000.00	\$18,000.00	\$10,000.00	\$30,000.00		
692	MOBILIZATION	U	1.00	\$50,000.00	\$50,000.00	\$56,000.00	\$56,000.00		
699	MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL	\$	2,000.00	\$1.00	\$2,000.00	\$1.00	\$2,000.00		
1008.11	ALTERATIONS AND ADDITIONS AS NEEDED - UNANTICIPATED WORK	\$	40,000.00	\$1.00	\$40,000.00	\$1.00	\$40,000.00		
1010.15	FUEL ADJUSTMENT	\$	10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00		

Totals:	\$407,675.00	\$568,245.00
Alt. Totals:		
Totals:	\$407,675.00	\$568,245.00



PS&E Comparison

TURNPIKE DRAINAGE
43303
NON-FEDERAL

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
Items								
203.1	COMMON EXCAVATION	CY	10.00	\$100.00	\$1,000.00	\$45.00	\$450.00	\$550.00
203.601	EMBANKMENT-IN-PLACE	CY	10.00	\$100.00	\$1,000.00	\$55.00	\$550.00	\$450.00
206.19	COMMON STRUCTURE EXCAVATION EXPLORATORY	CY	10.00	\$100.00	\$1,000.00	\$100.00	\$1,000.00	\$0.00
209.1	GRANULAR BACKFILL	CY	10.00	\$100.00	\$1,000.00	\$100.00	\$1,000.00	\$0.00
503.1	WATER DIVERSION STRUCTURES	U	1.00	\$15,000.00	\$15,000.00	\$7,500.00	\$7,500.00	\$7,500.00
571.1	REPAIRING AND POINTING STONE MASONRY	SY	7.00	\$500.00	\$3,500.00	\$400.00	\$2,800.00	\$700.00
585.3	STONE FILL, CLASS C	CY	22.00	\$150.00	\$3,300.00	\$90.00	\$1,980.00	\$1,320.00
593.411	GEOTEXTILE; PERM CONTROL CL.1, NON-WOVEN	SY	60.00	\$5.00	\$300.00	\$7.00	\$420.00	(\$120.00)
602.63515	UV CURED-IN-PLACE LINER FOR 15" PIPE	LF	130.00	\$300.00	\$39,000.00	\$350.00	\$45,500.00	(\$6,500.00)
602.63536	UV CURED-IN-PLACE LINER FOR 36" PIPE	LF	110.00	\$400.00	\$44,000.00	\$500.00	\$55,000.00	(\$11,000.00)
603.33212	12" CORR. POLYETHYLENE END SECTION	EA	5.00	\$360.00	\$1,800.00	\$750.00	\$3,750.00	(\$1,950.00)
603.40012	12" PIPE FOR SLOPE DRAINAGE	LF	190.00	\$170.00	\$32,300.00	\$70.00	\$13,300.00	\$19,000.00
604.0007	POLYETHYLENE LINER	EA	6.00	\$200.00	\$1,200.00	\$200.00	\$1,200.00	\$0.00
604.4	RECONSTRUCTING/ADJUSTING CATCH BASIN & DROP INLET	LF	4.00	\$1,400.00	\$5,600.00	\$625.00	\$2,500.00	\$3,100.00

PS&E Comparison

TURNPIKE DRAINAGE

43303

NON-FEDERAL

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
604.72	GRATES & FRAMES, TYPE B	EA	2.00	\$1,800.00	\$3,600.00	\$850.00	\$1,700.00	\$1,900.00
606.91	RESETTING OR SETTING GUARDRAIL	LF	50.00	\$200.00	\$10,000.00	\$45.00	\$2,250.00	\$7,750.00
611.05208	8" CEMENT LINED DUCTILE IRON WATER PIPE, CL 52	LF	25.00	\$335.00	\$8,375.00	\$120.00	\$3,000.00	\$5,375.00
611.70008	8" FITTING	EA	4.00	\$1,800.00	\$7,200.00	\$650.00	\$2,600.00	\$4,600.00
618.61	UNIFORMED OFFICERS WITH VEHICLE	\$	10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00	\$0.00
618.7	FLAGGERS	HR	40.00	\$100.00	\$4,000.00	\$40.00	\$1,600.00	\$2,400.00
619.1	MAINTENANCE OF TRAFFIC	U	1.00	\$35,000.00	\$35,000.00	\$30,000.00	\$30,000.00	\$5,000.00
619.25	PORTABLE CHANGEABLE MESSAGE SIGN	U	2.00	\$2,500.00	\$5,000.00	\$3,100.00	\$6,200.00	(\$1,200.00)
619.63	TRUCK-MOUNTED IMPACT ATTENUATOR, TEST LEVEL 3	U	1.00	\$7,500.00	\$7,500.00	\$15,000.00	\$15,000.00	(\$7,500.00)
622.1	STEEL WITNESS MARKERS	EA	9.00	\$100.00	\$900.00	\$200.00	\$1,800.00	(\$900.00)
645.44	TEMPORARY SLOPE MATTING TYPE D (WILDLIFE FRIENDLY)	SY	225.00	\$3.00	\$675.00	\$5.00	\$1,125.00	(\$450.00)
645.512	COMPOST SOCK FOR PERIMETER BERM	LF	765.00	\$8.00	\$6,120.00	\$8.00	\$6,120.00	\$0.00
645.531	SILT FENCE	LF	765.00	\$8.00	\$6,120.00	\$4.00	\$3,060.00	\$3,060.00
646.31	TURF ESTABLISHMENT WITH MULCH AND TACKIFIERS	SY	225.00	\$5.00	\$1,125.00	\$14.00	\$3,150.00	(\$2,025.00)
647.1	HUMUS	CY	78.00	\$85.00	\$6,630.00	\$40.00	\$3,120.00	\$3,510.00
670.0491	CONSTRUCT AND REMOVE TEMPORARY ACCESS ROAD	U	1.00	\$100,000.00	\$100,000.00	\$40,000.00	\$40,000.00	\$60,000.00



PS&E Comparison

TURNPIKE DRAINAGE
43303
NON-FEDERAL

Item No.	Description	Unit	Quantity	A-Bidder		PS&E		A-PS&E Difference
				Unit Price	Total	Unit Price	Total	
670.0492	CONSTRUCT AND REMOVE TEMPORARY ACCESS ROAD	U	1.00	\$33,000.00	\$33,000.00	\$10,000.00	\$10,000.00	\$23,000.00
670.0493	CONSTRUCT AND REMOVE TEMPORARY ACCESS ROAD	U	1.00	\$33,000.00	\$33,000.00	\$10,000.00	\$10,000.00	\$23,000.00
670.313	PIPE CLEAN OUT AND DEBRIS REMOVAL	U	3.00	\$10,000.00	\$30,000.00	\$6,000.00	\$18,000.00	\$12,000.00
692.	MOBILIZATION	U	1.00	\$56,000.00	\$56,000.00	\$50,000.00	\$50,000.00	\$6,000.00
699.	MISCELLANEOUS TEMPORARY EROSION AND SEDIMENT CONTROL	\$	2,000.00	\$1.00	\$2,000.00	\$1.00	\$2,000.00	\$0.00
1008.11	ALTERATIONS AND ADDITIONS AS NEEDED - UNANTICIPATED WORK	\$	40,000.00	\$1.00	\$40,000.00	\$1.00	\$40,000.00	\$0.00
1010.15	FUEL ADJUSTMENT	\$	10,000.00	\$1.00	\$10,000.00	\$1.00	\$10,000.00	\$0.00
Total:					\$566,245.00		\$407,675.00	\$158,570.00

March 28, 2023

SUPPLEMENTAL PROJECT INFORMATION SHEET

DESCRIPTION: The project is located along the US 202 (Spaulding) Connector from Chestnut Hill Road to NH Route 125, in Rochester with 2 specific locations. The first location is west of The Spaulding Connector near Chestnut Hill Road and the other east of the Spaulding Connector near the NH 125 overpass. On the westerly side of the project, near Chestnut Hill Road, five pipes will be slip-lined with cured in place liners; one 36" cmp under the roadway and four 15" cmps from median catch basins. In addition the 36" cmp pipe will require repair to the MRM headwall. On the easterly side of the project, near NH Route 125, five cmp slope pipes will be replaced with plastic slope pipes.

FEDERAL FUNDING: 0% (100% - Turnpike Funded from the Renewal and Replacement Program)

CONTINGENCY: The proposed contingency amount is 5% of the contract amount.


PROJECT INITIATED: This project was initiated through the Turnpikes Renewal and Replacement Program.

PROJECT EXPLANATION: The purpose of this project is to repair and replace ten existing metal drainage pipes along the US Route 202 Connector. These pipes are all corrugated metal which are deteriorated and are at the end of their expect life.

TRAFFIC IMPLICATION: The project will have minimal traffic implications. To access the slope pipes, an access road will be used for all but one installation. The remaining pipe will require access from the ramp.

FINAL COMPLETION DATE: September 29, 2023.

TURNPIKE DRAINAGE - 43303

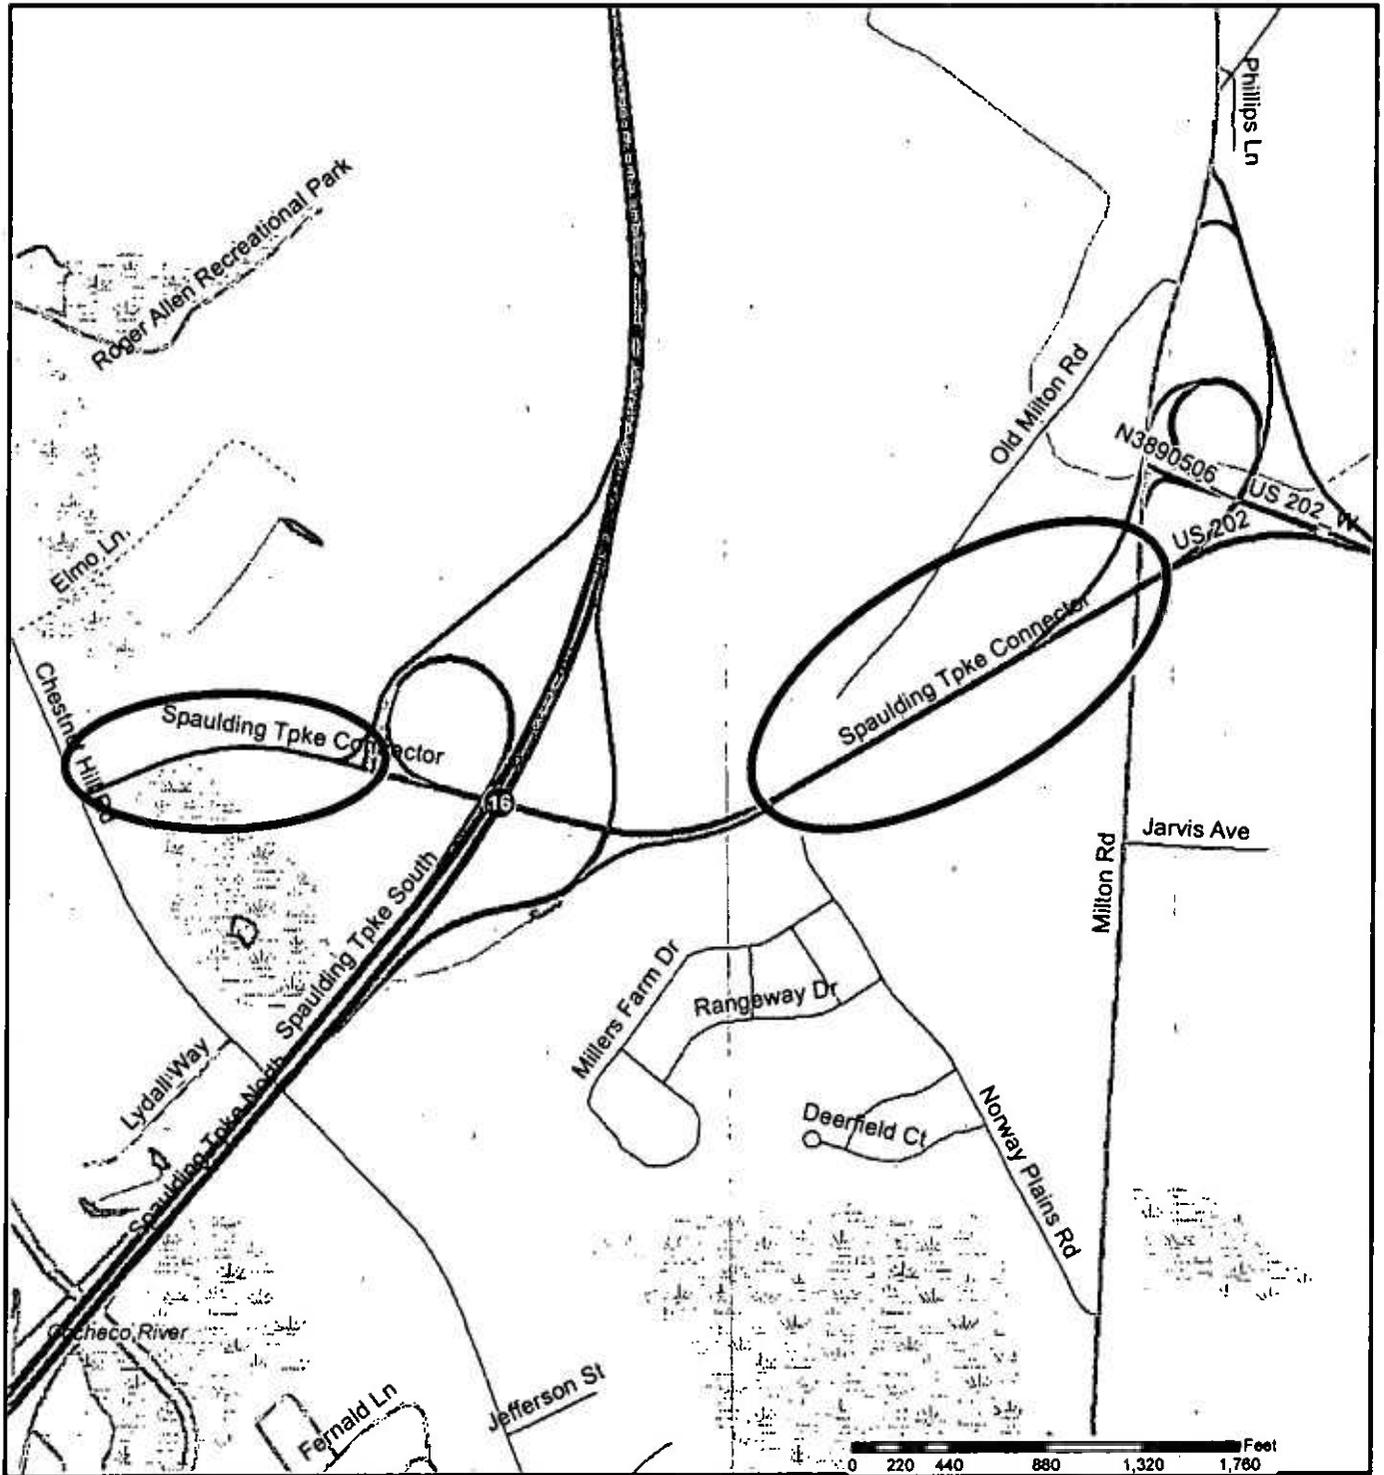

LEGEND


- Streams
- Water Bodies
- US Routes
- State Routes
- Interstates
- Local Roads
- Town Boundary

New Hampshire
DOT
 Department of Transportation

State #: 43303

Federal #: N/A

LOCATION MAP

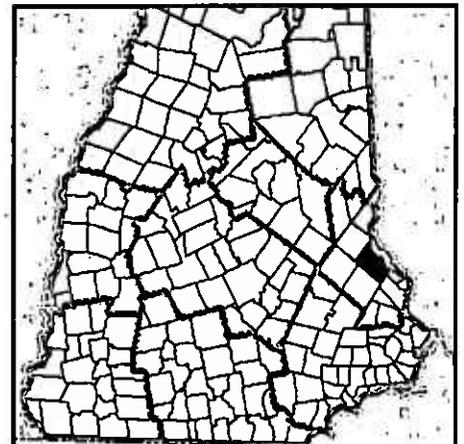

State of New Hampshire

Department of State

CERTIFICATE

I, David M. Scanlan, Secretary of State of the State of New Hampshire, do hereby certify that S.U.R. CONSTRUCTION, INC. is a New Hampshire Profit Corporation registered to transact business in New Hampshire on January 28, 1987. I further certify that all fees and documents required by the Secretary of State's office have been received and is in good standing as far as this office is concerned.

Business ID: 108192

Certificate Number: 0006219581



IN TESTIMONY WHEREOF,
I hereto set my hand and cause to be affixed
the Seal of the State of New Hampshire,
this 1st day of May A.D. 2023.

A handwritten signature in black ink, appearing to read "David M. Scanlan".

David M. Scanlan
Secretary of State

CERTIFICATE OF VOTE

I, Andrew G. LePage Hereby certify that I am duly elected
Vice President of S.U.R. CONSTRUCTION, INC.

I hereby certify the following is a true copy of a vote taken at a meeting
of the Board of Directors of the Corporation, duly called and held
on May 1, 2023, at which a quorum of the Board was present
and voting.

VOTED: That Jason deWildt is duly authorized
to enter into a specific contract namely TURNPIKE DRAINAGE 43303
With State of New Hampshire, and further authorized to
Department of Transportation
execute any documents which may in his judgment be desirable or necessary to effect
the purpose of this vote.

I hereby certify that said vote has not been amended or repealed and remains
in full force and effect as of May 1, 2023, and that
Jason deWildt is duly elected Vice President of this
Corporation.

DATED: May 1, 2023

ATTEST:  (Affix Corp. Seal)
Andrew G. LePage, Vice President



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)
5/1/2023

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER THE ROWLEY AGENCY INC. 45 Constitution Avenue P.O. Box 511 Concord NH 03302-0511		CONTACT NAME: Peggy Johnson PHONE (A/C No. Ext): (603) 224-2562 FAX (A/C, No): (603) 224-8012 E-MAIL ADDRESS: pjohnson@rowleyagency.com	
INSURED S.U.R. Construction, Inc. P.O. Box 720 Rochester NH 03866-0720		INSURER(S) AFFORDING COVERAGE INSURER A: Firemen's Ins Co of Wash. DC NAIC # 21784 INSURER B: Acadia Insurance Company 31325 INSURER C: INSURER D: INSURER E: INSURER F:	

COVERAGES **CERTIFICATE NUMBER:** **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSR	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PROJECT <input type="checkbox"/> LOC OTHER:			CPA100075841	3/31/2023	3/31/2024	EACH OCCURRENCE \$ 1,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$ 300,000 MED EXP (Any one person) \$ 10,000 PERSONAL & ADV INJURY \$ 1,000,000 GENERAL AGGREGATE \$ 2,000,000 PRODUCTS - COM/OP AGG \$ 2,000,000
A	AUTOMOBILE LIABILITY <input checked="" type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input checked="" type="checkbox"/> HIRED AUTOS <input checked="" type="checkbox"/> NON-OWNED AUTOS <input type="checkbox"/> CA9948			CAA100075941	3/31/2023	3/31/2024	COMBINED SINGLE LIMIT (Ea accident) \$ 1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ Medical payments \$
B	<input checked="" type="checkbox"/> UMBRELLA LIAB <input checked="" type="checkbox"/> OCCUR <input type="checkbox"/> EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE DED <input checked="" type="checkbox"/> RETENTION \$ 0			CUA100076042	3/31/2023	3/31/2024	EACH OCCURRENCE \$ 5,000,000 AGGREGATE \$ 5,000,000 Completed Ops Aggregate \$ 5,000,000
A	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below		Y/N N	3A States: NH, ME, MA WPA100076142	3/31/2023	3/31/2024	<input checked="" type="checkbox"/> PER STATUTE <input type="checkbox"/> OTHER E.L. EACH ACCIDENT \$ 250,000 E.L. DISEASE - EA EMPLOYEE \$ 250,000 E.L. DISEASE - POLICY LIMIT \$ 500,000
A	Leased/Rented Equipment			CTM010912334	3/31/2023	3/31/2024	\$1,000,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)
Turnpike Drainage 43303. State of NH DOT is additional insured under the general liability when required by written contract.

CERTIFICATE HOLDER State of NH DOT POB 483 Concord, NH 03302-0483	CANCELLATION SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS. AUTHORIZED REPRESENTATIVE Peggy Johnson/PAJ <i>Peggy C. Johnson</i>
---	---



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)

5/1/2023

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER THE ROWLEY AGENCY INC. 45 Constitution Avenue P.O. Box 511 Concord NH 03302-0511	CONTACT NAME: Peggy Johnson PHONE (A/C No. Ext): (603) 224-2562 FAX (A/C. No.): (603) 224-8012 E-MAIL ADDRESS: pjohnson@rowleyagency.com	
	INSURER(S) AFFORDING COVERAGE	
INSURED State of NH DOT POB 483 Concord NH 03302-0483	INSURER A: Acadia Insurance Company NAIC # 31325	
	INSURER B:	
	INSURER C:	
	INSURER D:	
	INSURER E:	
	INSURER F:	

COVERAGES **CERTIFICATE NUMBER:** **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADOL INSD	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR <input checked="" type="checkbox"/> Owners & Contractors Protective GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC OTHER:			0CP4655454	5/1/2023	5/1/2024	EACH OCCURRENCE \$ 1,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$ MED EXP (Any one person) \$ PERSONAL & ADV INJURY \$ GENERAL AGGREGATE \$ 2,000,000 PRODUCTS - COMP/OP AGG \$ OTHER \$
	AUTOMOBILE LIABILITY <input type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> HIRED AUTOS <input type="checkbox"/> NON-OWNED AUTOS						COMBINED SINGLE LIMIT (Ea accident) \$ BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ OTHER \$
	<input type="checkbox"/> UMBRELLA LIAB <input type="checkbox"/> OCCUR <input type="checkbox"/> EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE <input type="checkbox"/> DED <input type="checkbox"/> RETENTION \$						EACH OCCURRENCE \$ AGGREGATE \$ OTHER \$
	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below		Y/N	N/A			<input type="checkbox"/> PER STATUTE <input type="checkbox"/> OTH-ER E.L. EACH ACCIDENT \$ E.L. DISEASE - EA EMPLOYEE \$ E.L. DISEASE - POLICY LIMIT \$

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)

Turnpike Drainage 43303.
 Contractor: S.U.R. Construction.

CERTIFICATE HOLDER**CANCELLATION**

State of NH DOT POB 483 Concord, NH 03302-0483	SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS. AUTHORIZED REPRESENTATIVE Peggy Johnson/PAJ <i>Peggy A Johnson</i>
--	---

© 1988-2014 ACORD CORPORATION. All rights reserved.
